ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
1	**1 FiberTel Infrastructure &**	**343.25 hrs**	**0 hrs**	**343.25 hrs**	**0 hrs**	**343.25 hrs**	**0%**
2	**1.1 Initiate Project**	**32.5 hrs**	**0 hrs**	**32.5 hrs**	**0 hrs**	**32.5 hrs**	**0%**
3	1.1.1 Kickoff Mee	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
4	1.1.2 Meeting with Management, team and	10.5 hrs	0 hrs	10.5 hrs	0 hrs	10.5 hrs	0%
5	1.1.3 Develop Project Charter	5 hrs	0 hrs	5 hrs	0 hrs	5 hrs	0%
6	1.1.4 Review and approval of project charter	14 hrs	0 hrs	14 hrs	0 hrs	14 hrs	0%
7	1.2 Team Meeting for Project Plan	3.5 hrs	0 hrs	3.5 hrs	0 hrs	3.5 hrs	0%
8	**1.3 Planning**	**39.75 hrs**	**0 hrs**	**39.75 hrs**	**0 hrs**	**39.75 hrs**	**0%**
9	**1.3.1 Requireme**	**13.5 hrs**	**0 hrs**	**13.5 hrs**	**0 hrs**	**13.5 hrs**	**0%**
10	1.3.1.1 Obtain input from Procurement Dept (FiberTel) on	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%

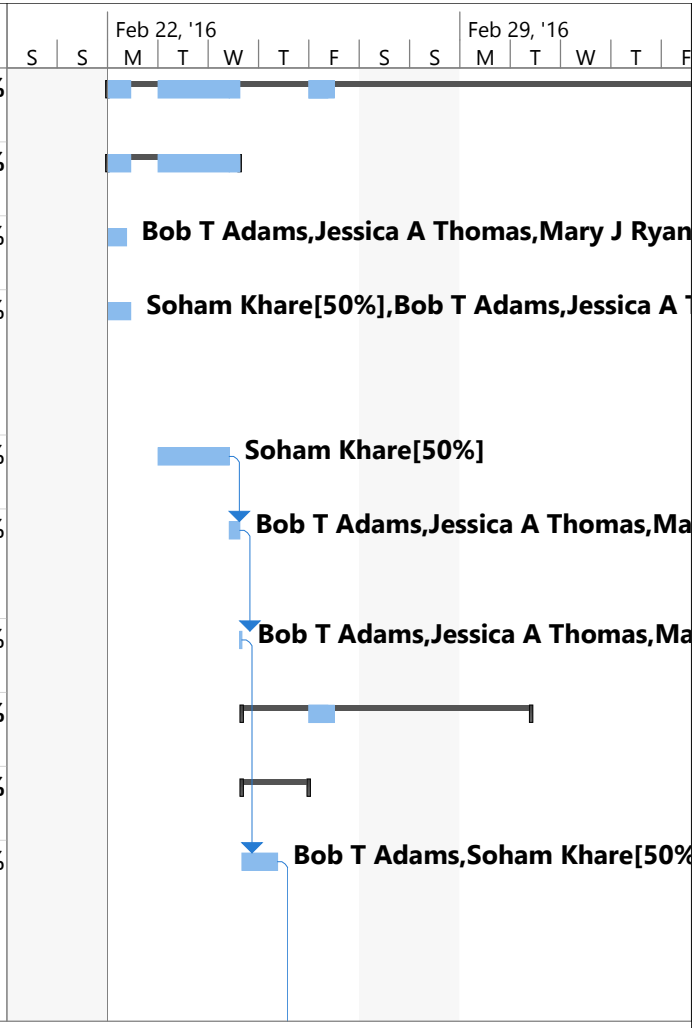

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Progress	
Project Summary	Manual Summary	Manual Progress	
Inactive Task	Start-only		
Inactive Milestone	Finish-only		

ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
11	1.3.1.2 Obtain client input(FiberTel) on the PCs	4.5 hrs	0 hrs	4.5 hrs	0 hrs	4.5 hrs	0%
12	1.3.1.3 Obtain Client input (FiberTel) on the transition assistance to	4.5 hrs	0 hrs	4.5 hrs	0 hrs	4.5 hrs	0%
13	1.3.1.4 Obtain client input for Adirondack's	1.5 hrs	0 hrs	1.5 hrs	0 hrs	1.5 hrs	0%
14	**1.3.2 Assessment of**	**26.25 hrs**	**0 hrs**	**26.25 hrs**	**0 hrs**	**26.25 hrs**	**0%**
15	1.3.2.1 Determine Network	6 hrs	0 hrs	6 hrs	0 hrs	6 hrs	0%
16	1.3.2.2 Verify Internet Access	1.5 hrs	0 hrs	1.5 hrs	0 hrs	1.5 hrs	0%
17	1.3.2.3 Determine Furniture	4.5 hrs	0 hrs	4.5 hrs	0 hrs	4.5 hrs	0%
18	1.3.2.4 Document specific	6 hrs	0 hrs	6 hrs	0 hrs	6 hrs	0%

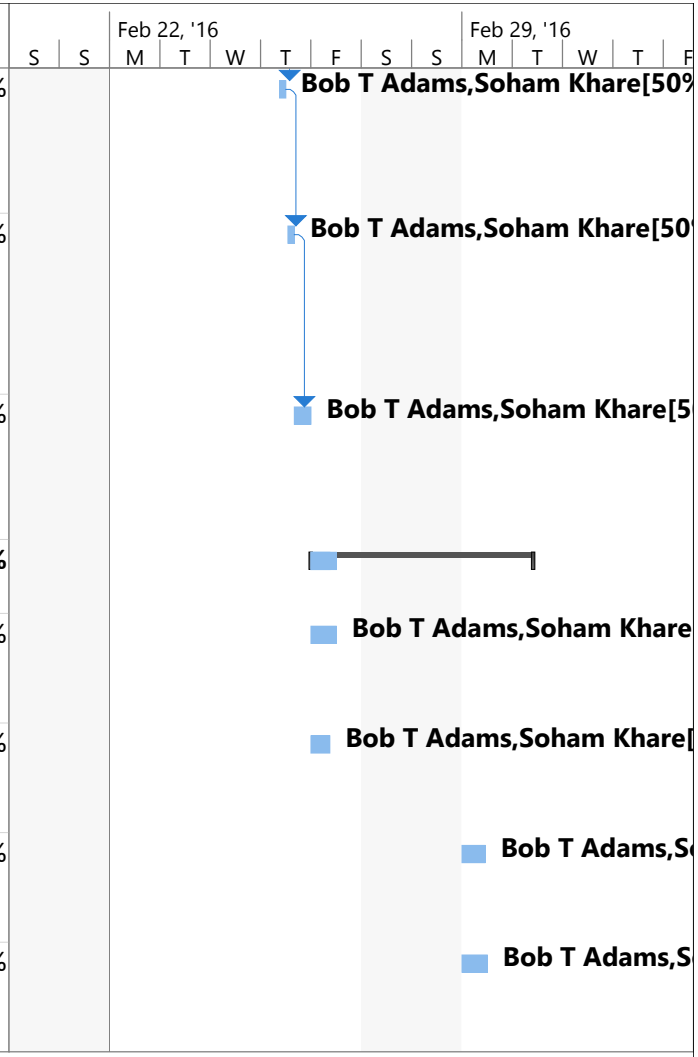

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Progress	
Project Summary	Manual Summary	Manual Progress	
Inactive Task	Start-only		
Inactive Milestone	Finish-only		

ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
19	1.3.2.5 Finalize design of new	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
20	1.3.2.6 Verify required software	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
21	1.3.2.7 Verify required network	2.25 hrs	0 hrs	2.25 hrs	0 hrs	2.25 hrs	0%
22	1.4 Team Meeting for Procurement	7 hrs	0 hrs	7 hrs	0 hrs	7 hrs	0%
23	**1.5 Procurement**	**32 hrs**	**0 hrs**	**32 hrs**	**0 hrs**	**32 hrs**	**0%**
24	**1.5.1 Procureme**	**18 hrs**	**0 hrs**	**18 hrs**	**0 hrs**	**18 hrs**	**0%**
25	1.5.1.1 Build list of	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
26	1.5.1.2 Obtain cost	8 hrs	0 hrs	8 hrs	0 hrs	8 hrs	0%
27	1.5.1.3 Refine and adjust	4 hrs	0 hrs	4 hrs	0 hrs	4 hrs	0%
28	1.5.1.4 Finalize	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%

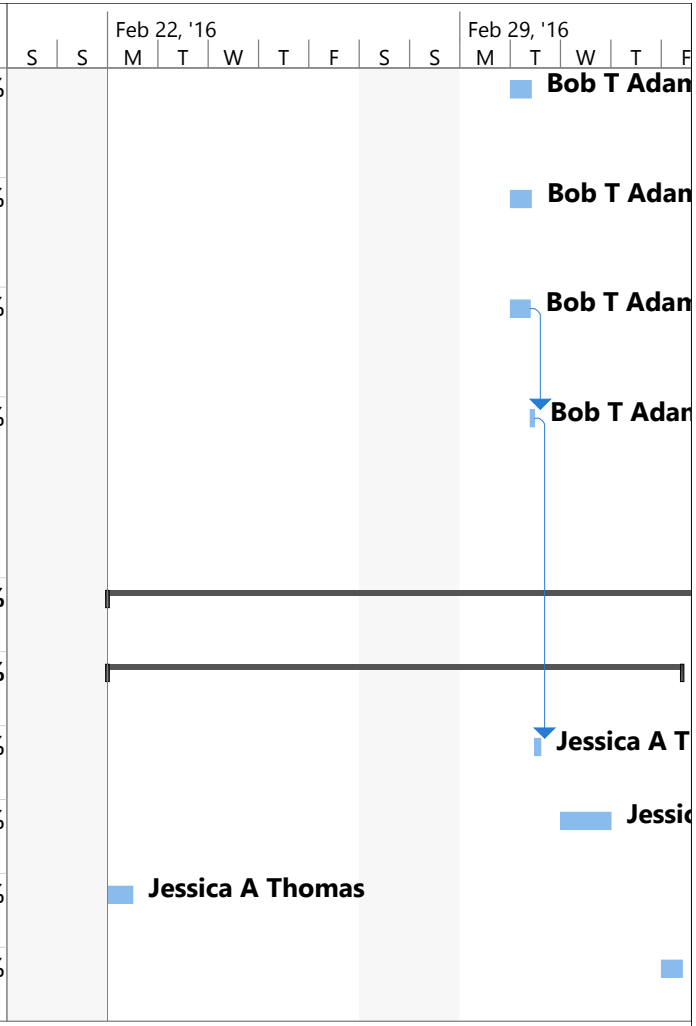

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
29	1.5.1.5 Determine	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
30	**1.5.2 Place order**	**13 hrs**	**0 hrs**	**13 hrs**	**0 hrs**	**13 hrs**	**0%**
31	1.5.2.1 Issue purchase	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
32	1.5.2.2 Issue purchase	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
33	1.5.2.3 Verify correctness of	4 hrs	0 hrs	4 hrs	0 hrs	4 hrs	0%
34	1.5.2.4 Verify correctness of	4 hrs	0 hrs	4 hrs	0 hrs	4 hrs	0%
35	1.5.3 Procure Linux Server	1 hr	0 hrs	1 hr	0 hrs	1 hr	0%
36	1.6 Team Meeting f	7 hrs	0 hrs	7 hrs	0 hrs	7 hrs	0%
37	**1.7 Execution**	**141.5 hrs**	**0 hrs**	**141.5 hrs**	**0 hrs**	**141.5 hrs**	**0%**
38	**1.7.1 Assemble Furniture &**	**52.5 hrs**	**0 hrs**	**52.5 hrs**	**0 hrs**	**52.5 hrs**	**0%**
39	1.7.1.1 Place new furniture in Final	16 hrs	0 hrs	16 hrs	0 hrs	16 hrs	0%
40	1.7.1.2 Assemble and verify	20 hrs	0 hrs	20 hrs	0 hrs	20 hrs	0%

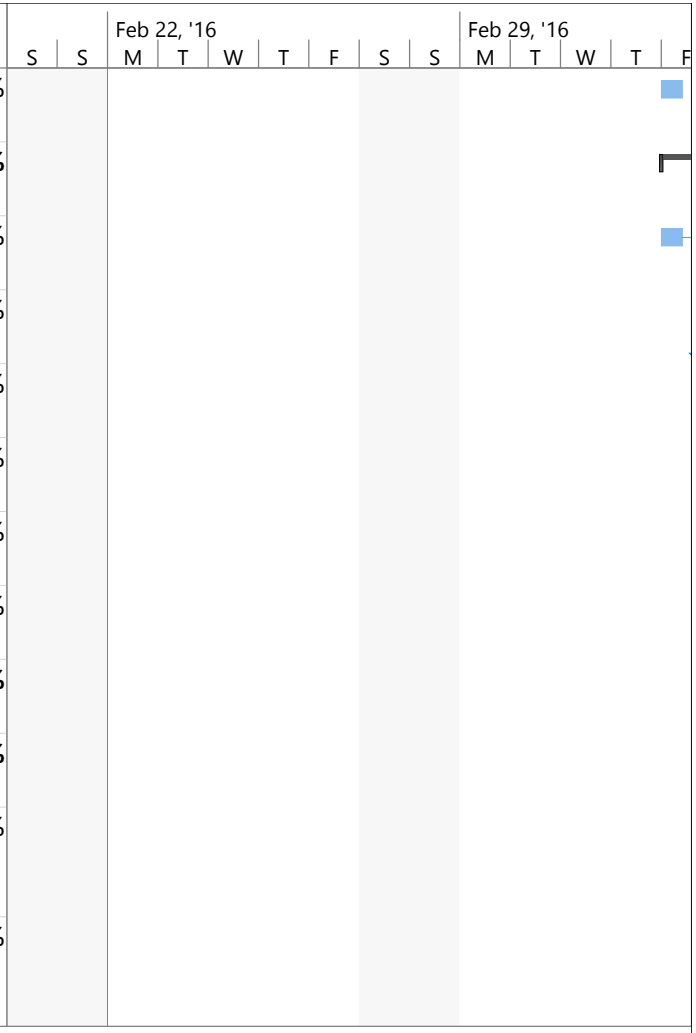

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Progress	
Project Summary	Manual Summary	Manual Progress	
Inactive Task	Start-only		
Inactive Milestone	Finish-only		

ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
41	1.7.1.3 Assemble and verify operation of	7.5 hrs	0 hrs	7.5 hrs	0 hrs	7.5 hrs	0%
42	1.7.1.4 Assemble and test new scanner /	9 hrs	0 hrs	9 hrs	0 hrs	9 hrs	0%
43	**1.7.2 Install & connect**	**34 hrs**	**0 hrs**	**34 hrs**	**0 hrs**	**34 hrs**	**0%**
44	1.7.2.1 Install Cisco ME	1 hr	0 hrs	1 hr	0 hrs	1 hr	0%
45	1.7.2.2 Connect	1 hr	0 hrs	1 hr	0 hrs	1 hr	0%
46	1.7.2.3 Install network	24 hrs	0 hrs	24 hrs	0 hrs	24 hrs	0%
47	1.7.2.4 Connect	6 hrs	0 hrs	6 hrs	0 hrs	6 hrs	0%
48	1.7.2.5 Connect	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
49	1.7.3 Install Linux server for MetroTech	7.5 hrs	0 hrs	7.5 hrs	0 hrs	7.5 hrs	0%
50	**1.7.4 Configure & Install the assembled**	**45.5 hrs**	**0 hrs**	**45.5 hrs**	**0 hrs**	**45.5 hrs**	**0%**

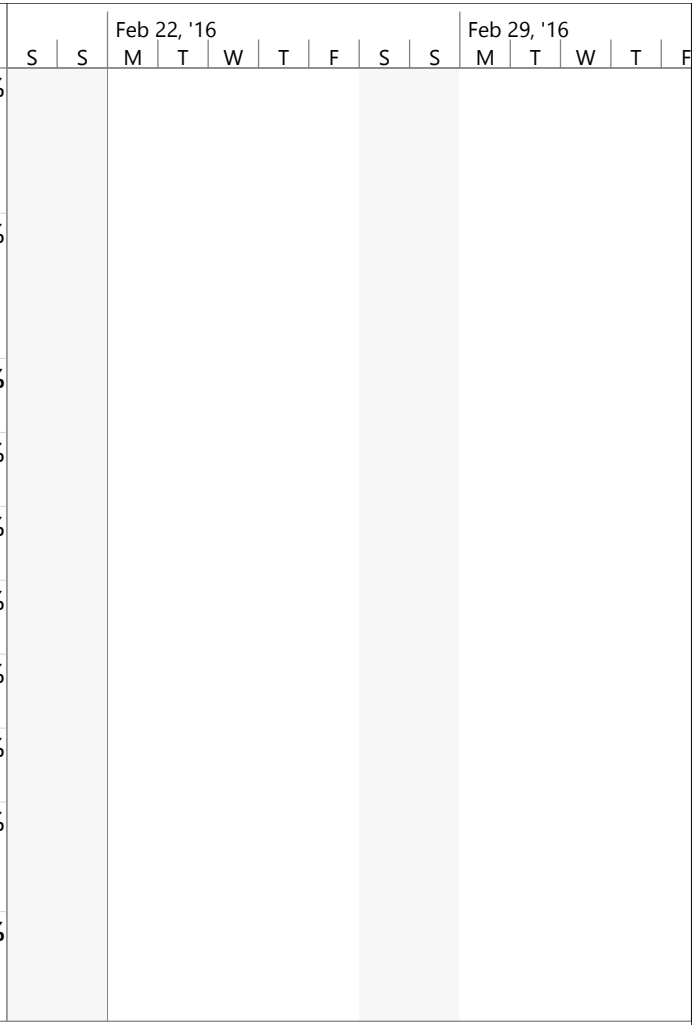

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
51	1.7.4.1 Configure and Test each individual PC workstation	5.25 hrs	0 hrs	5.25 hrs	0 hrs	5.25 hrs	0%
52	1.7.4.2 Configure and Test each individual VoIP handset	8.75 hrs	0 hrs	8.75 hrs	0 hrs	8.75 hrs	0%
53	1.7.4.3 Install and Test Copier/printer	7 hrs	0 hrs	7 hrs	0 hrs	7 hrs	0%
54	1.7.4.4 Install and configure Wireless Access points	7 hrs	0 hrs	7 hrs	0 hrs	7 hrs	0%
55	1.7.4.5 Install required software on New PCs	17.5 hrs	0 hrs	17.5 hrs	0 hrs	17.5 hrs	0%
56	1.7.5 Cable Management	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%



Project: FiberTel Infrastructure
Date: Sun 4/17/16



ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
57	1.8 Team Meeting f	7 hrs	0 hrs	7 hrs	0 hrs	7 hrs	0%
58	**1.9 Testing**	**29 hrs**	**0 hrs**	**29 hrs**	**0 hrs**	**29 hrs**	**0%**
59	1.9.1 Verify operation of Wired Network	6 hrs	0 hrs	6 hrs	0 hrs	6 hrs	0%
60	1.9.2 Verify operation of Wireless Network	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
61	1.9.3 Test copier/printer for network connectivity	3 hrs	0 hrs	3 hrs	0 hrs	3 hrs	0%
62	1.9.4 Test the functioning of the Linux server	4.5 hrs	0 hrs	4.5 hrs	0 hrs	4.5 hrs	0%
63	1.9.5 Test the operation of the	6 hrs	0 hrs	6 hrs	0 hrs	6 hrs	0%
64	1.9.6 Verify correct	2 hrs	0 hrs	2 hrs	0 hrs	2 hrs	0%
65	1.9.7 Test network connectivity	4.5 hrs	0 hrs	4.5 hrs	0 hrs	4.5 hrs	0%

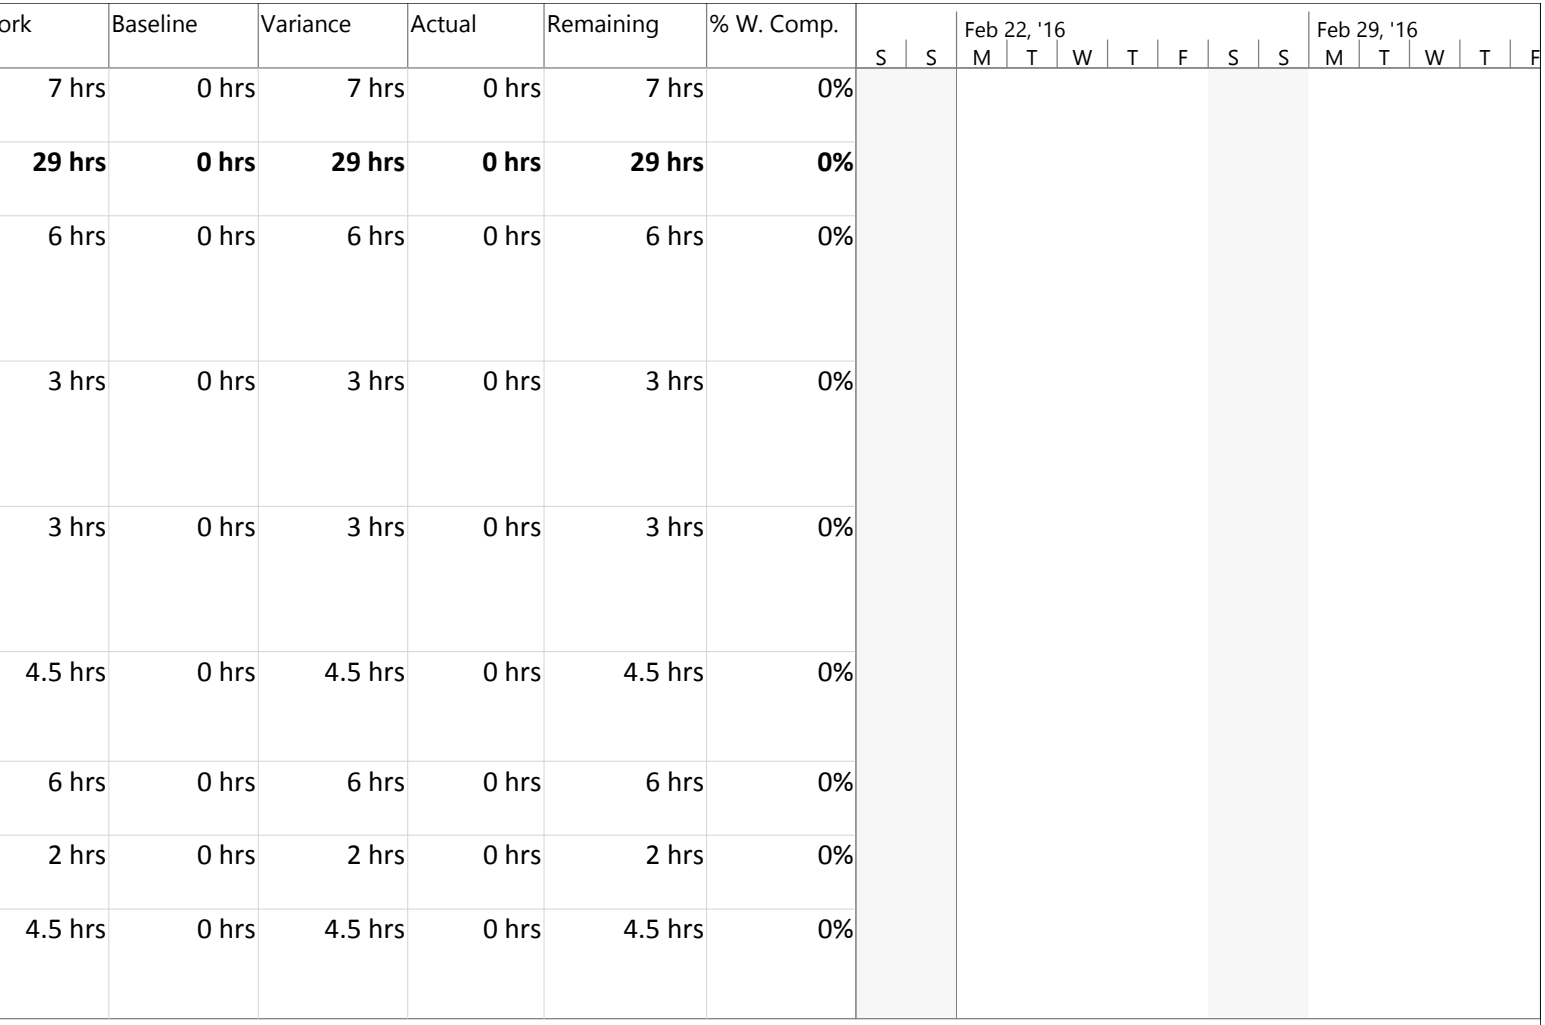

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress

ID	Task Name	Work	Baseline	Variance	Actual	Remaining	% W. Comp.
66	1.10 Team meeting for project	3.5 hrs	0 hrs	3.5 hrs	0 hrs	3.5 hrs	0%
67	**1.11 Documentatio**	**40 hrs**	**0 hrs**	**40 hrs**	**0 hrs**	**40 hrs**	**0%**
68	1.11.1 Develop written	40 hrs	0 hrs	40 hrs	0 hrs	40 hrs	0%
69	1.12 Project close meeting with	0.5 hrs	0 hrs	0.5 hrs	0 hrs	0.5 hrs	0%

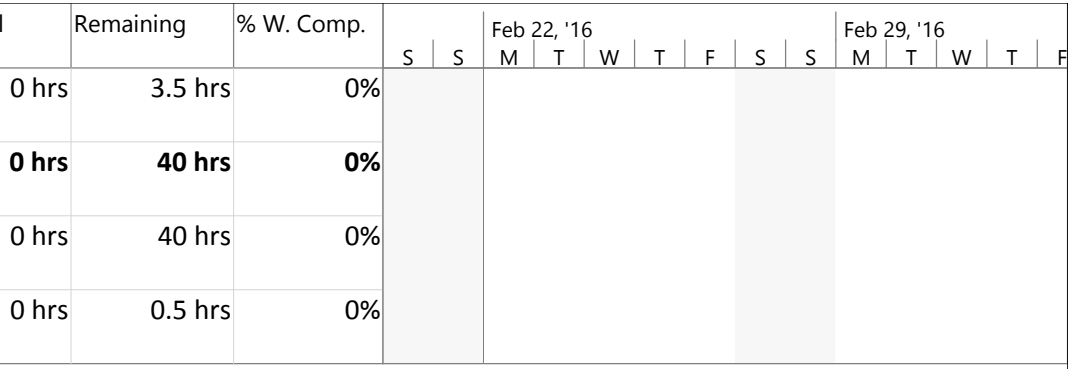

Project: FiberTel Infrastructure
Date: Sun 4/17/16



Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

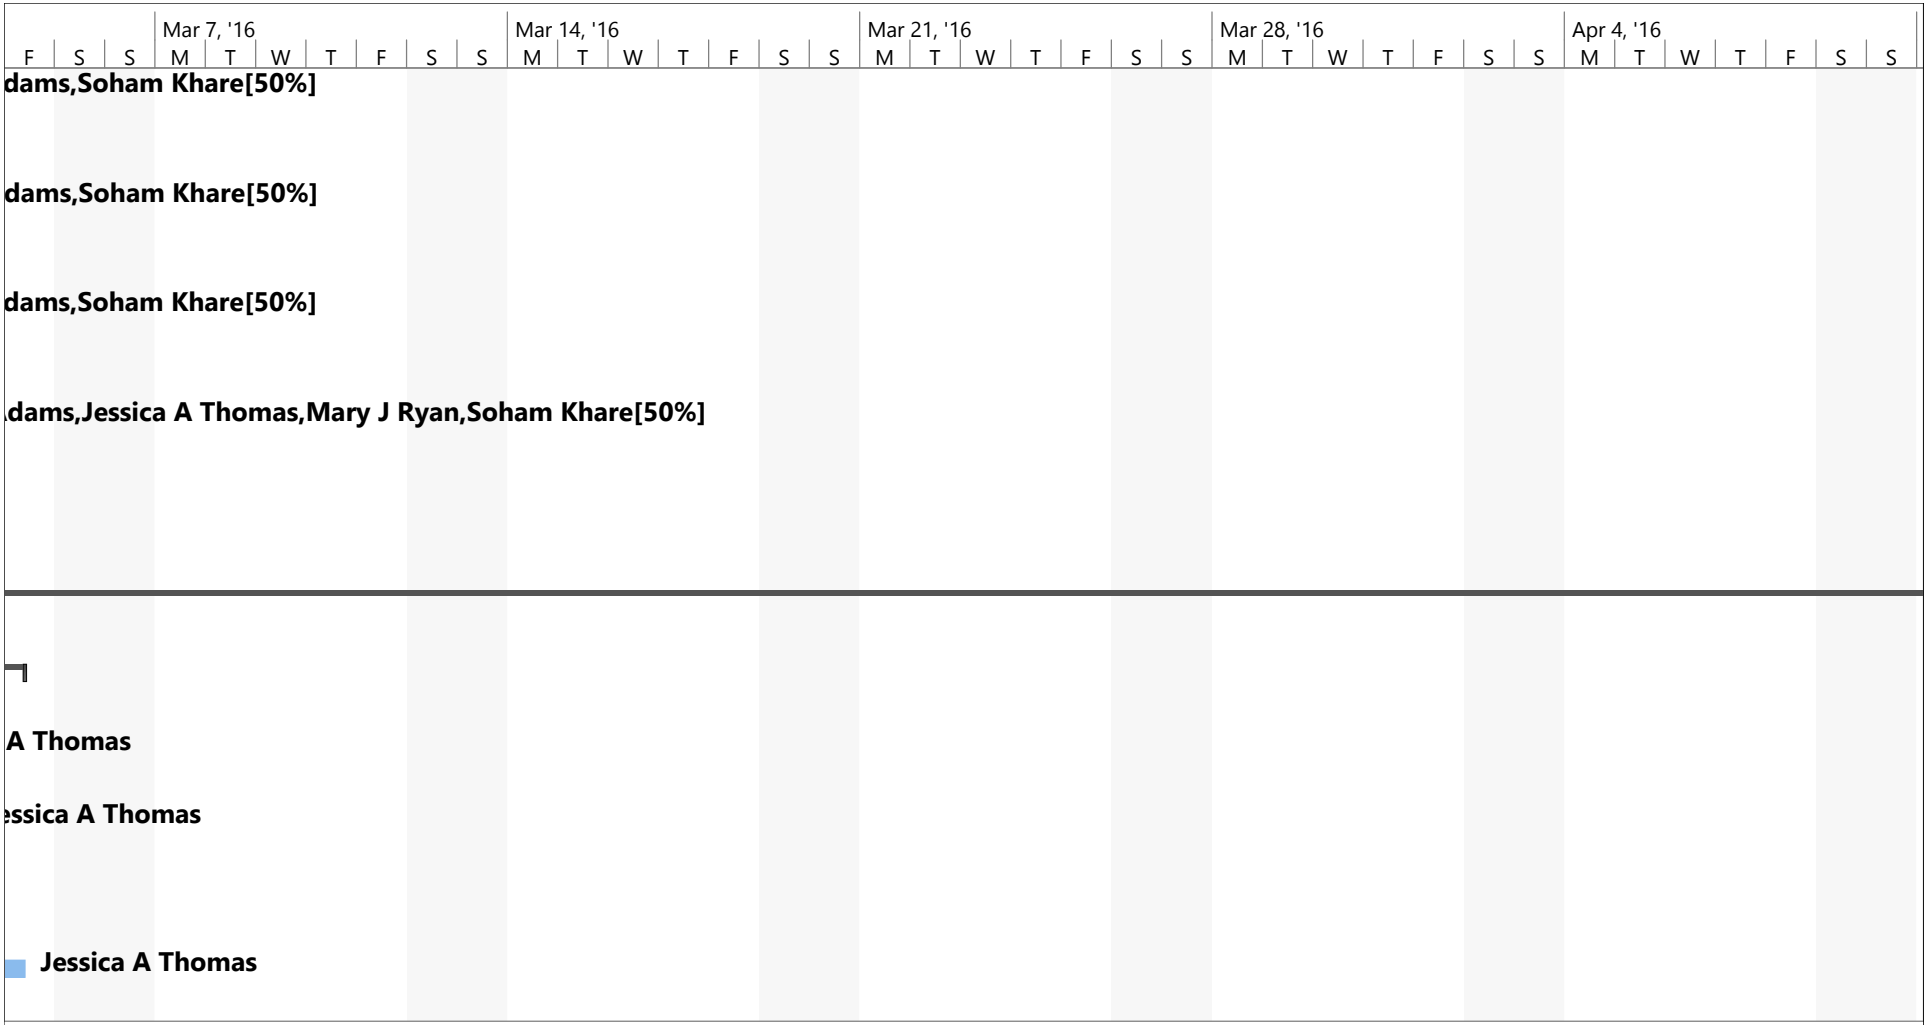

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

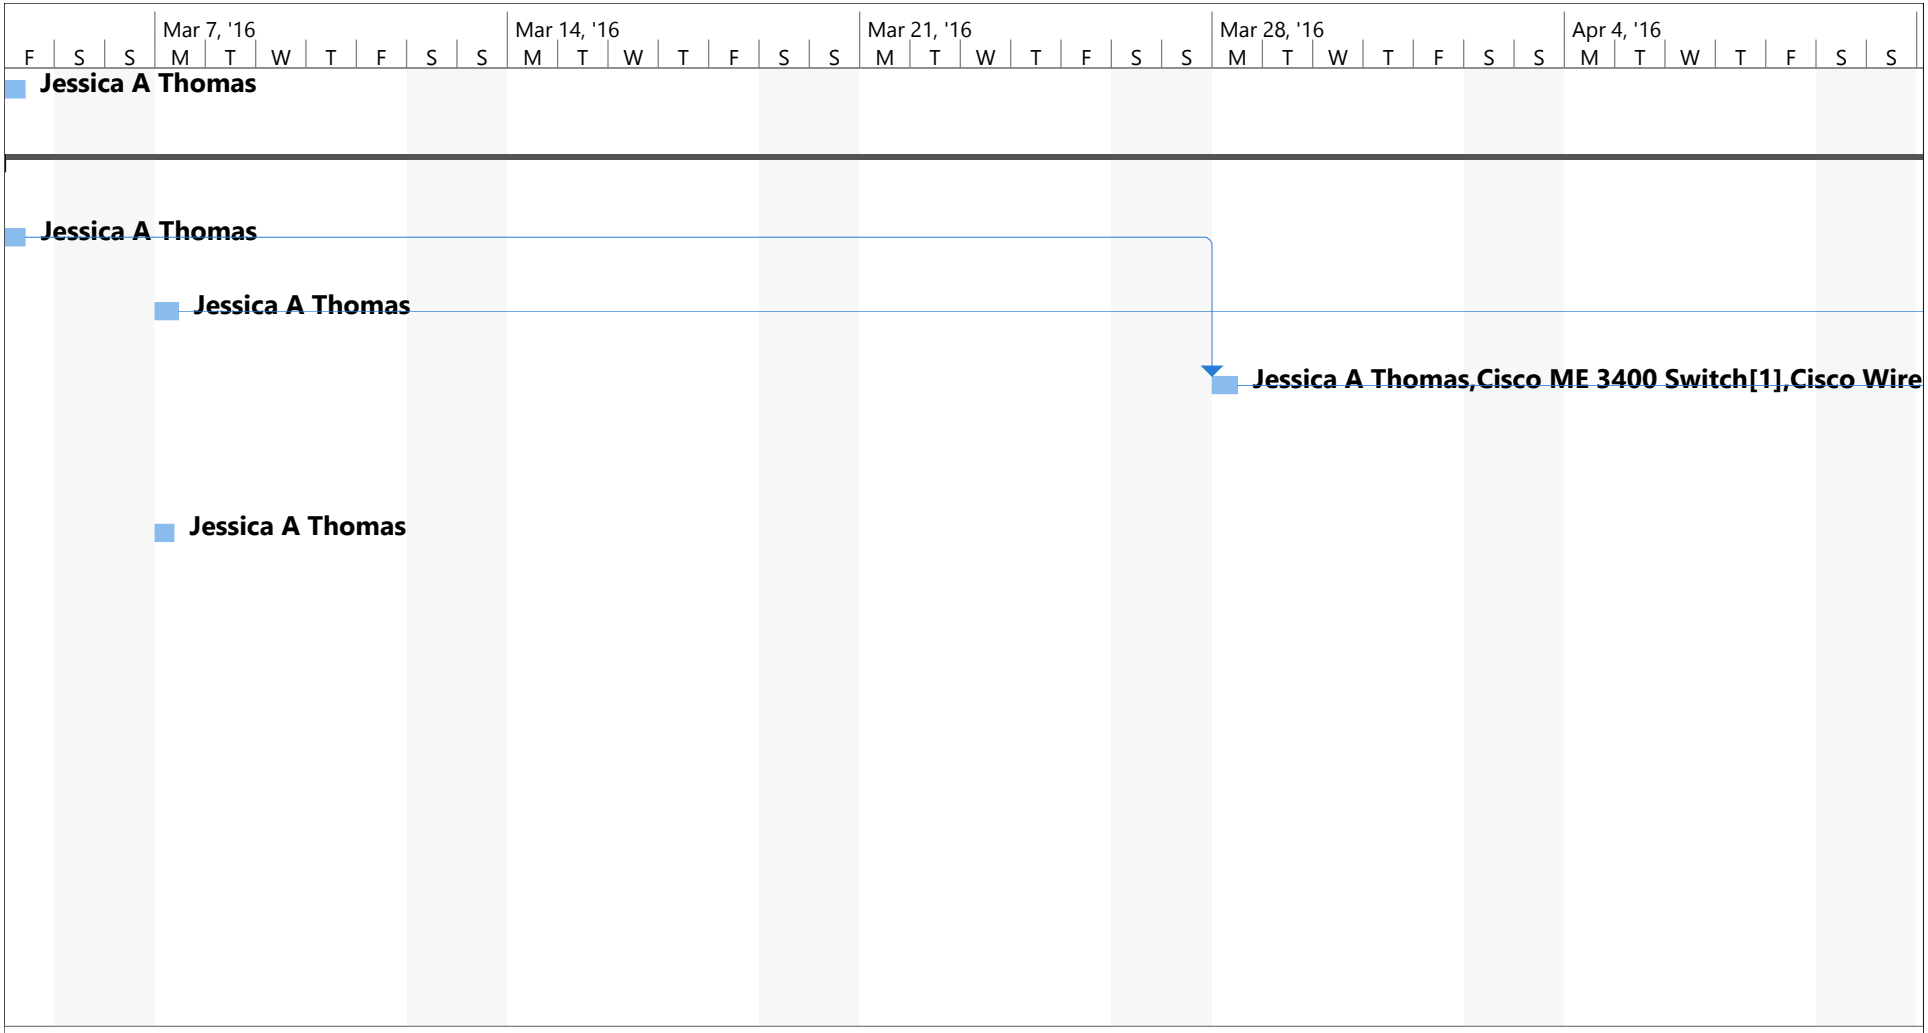

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

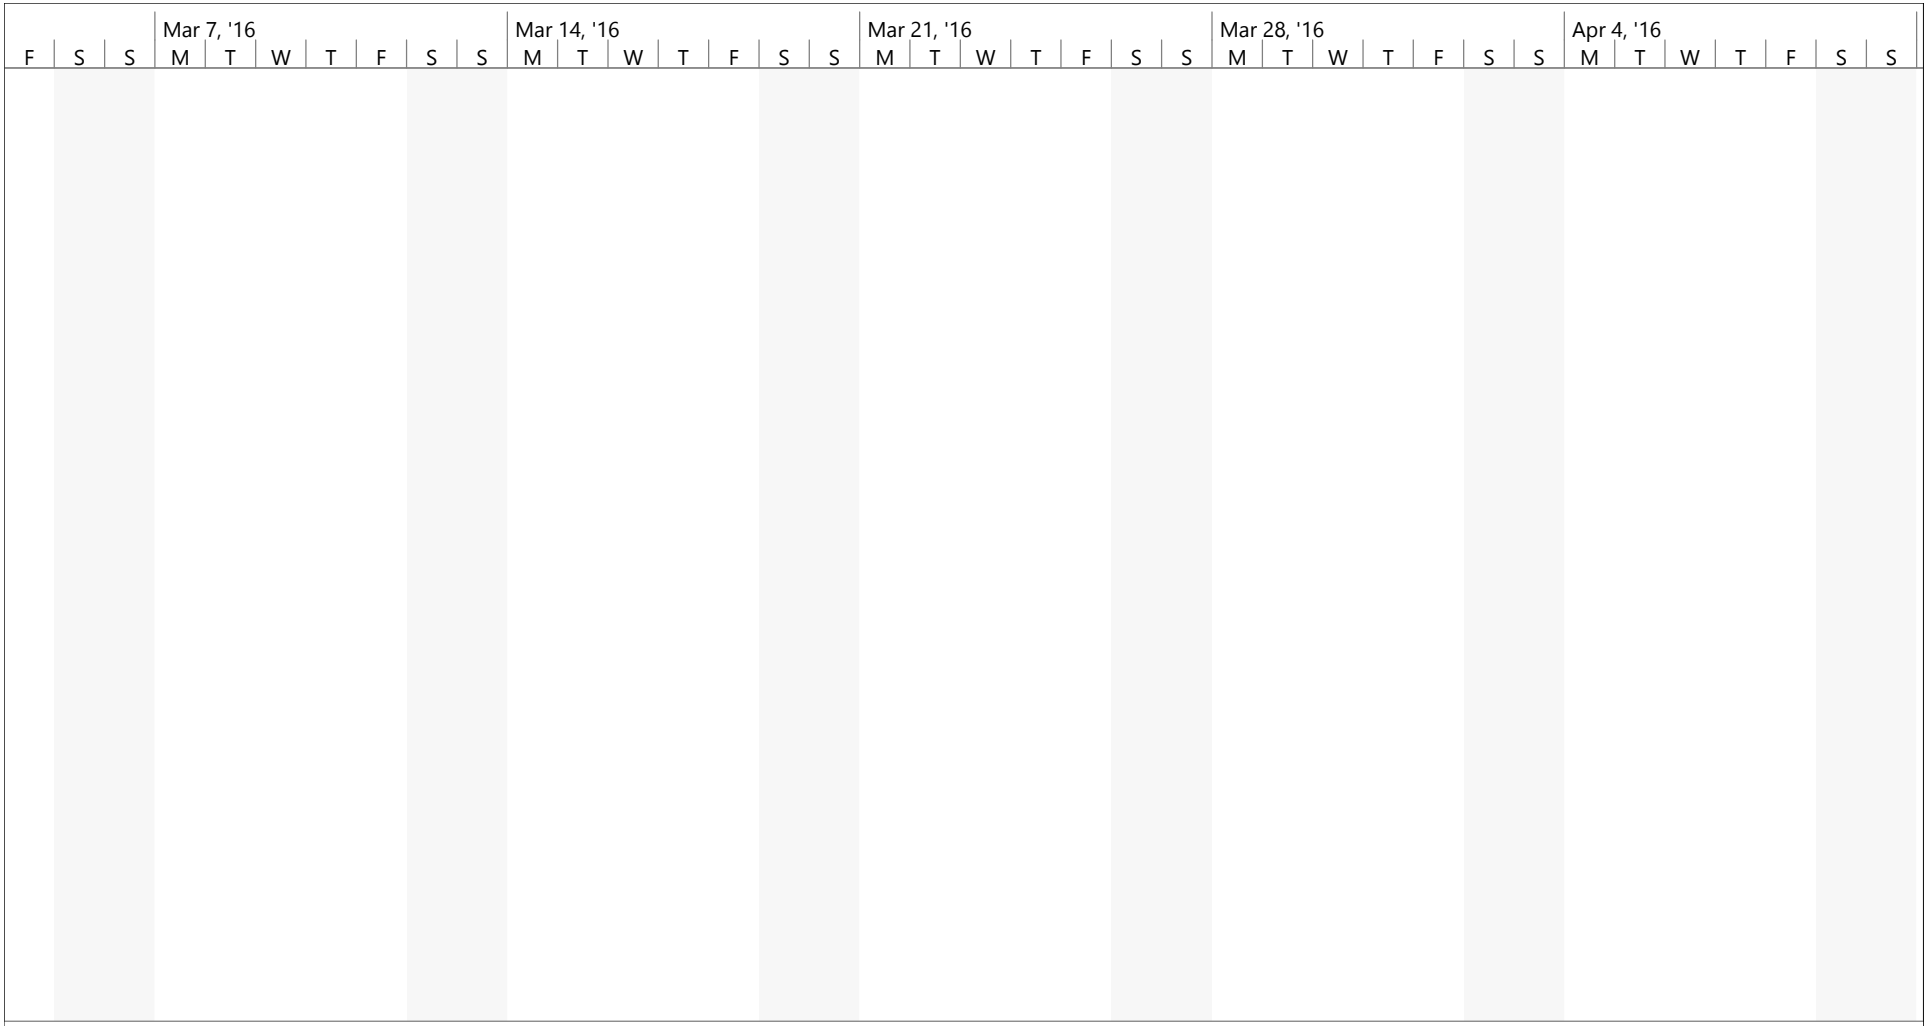

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

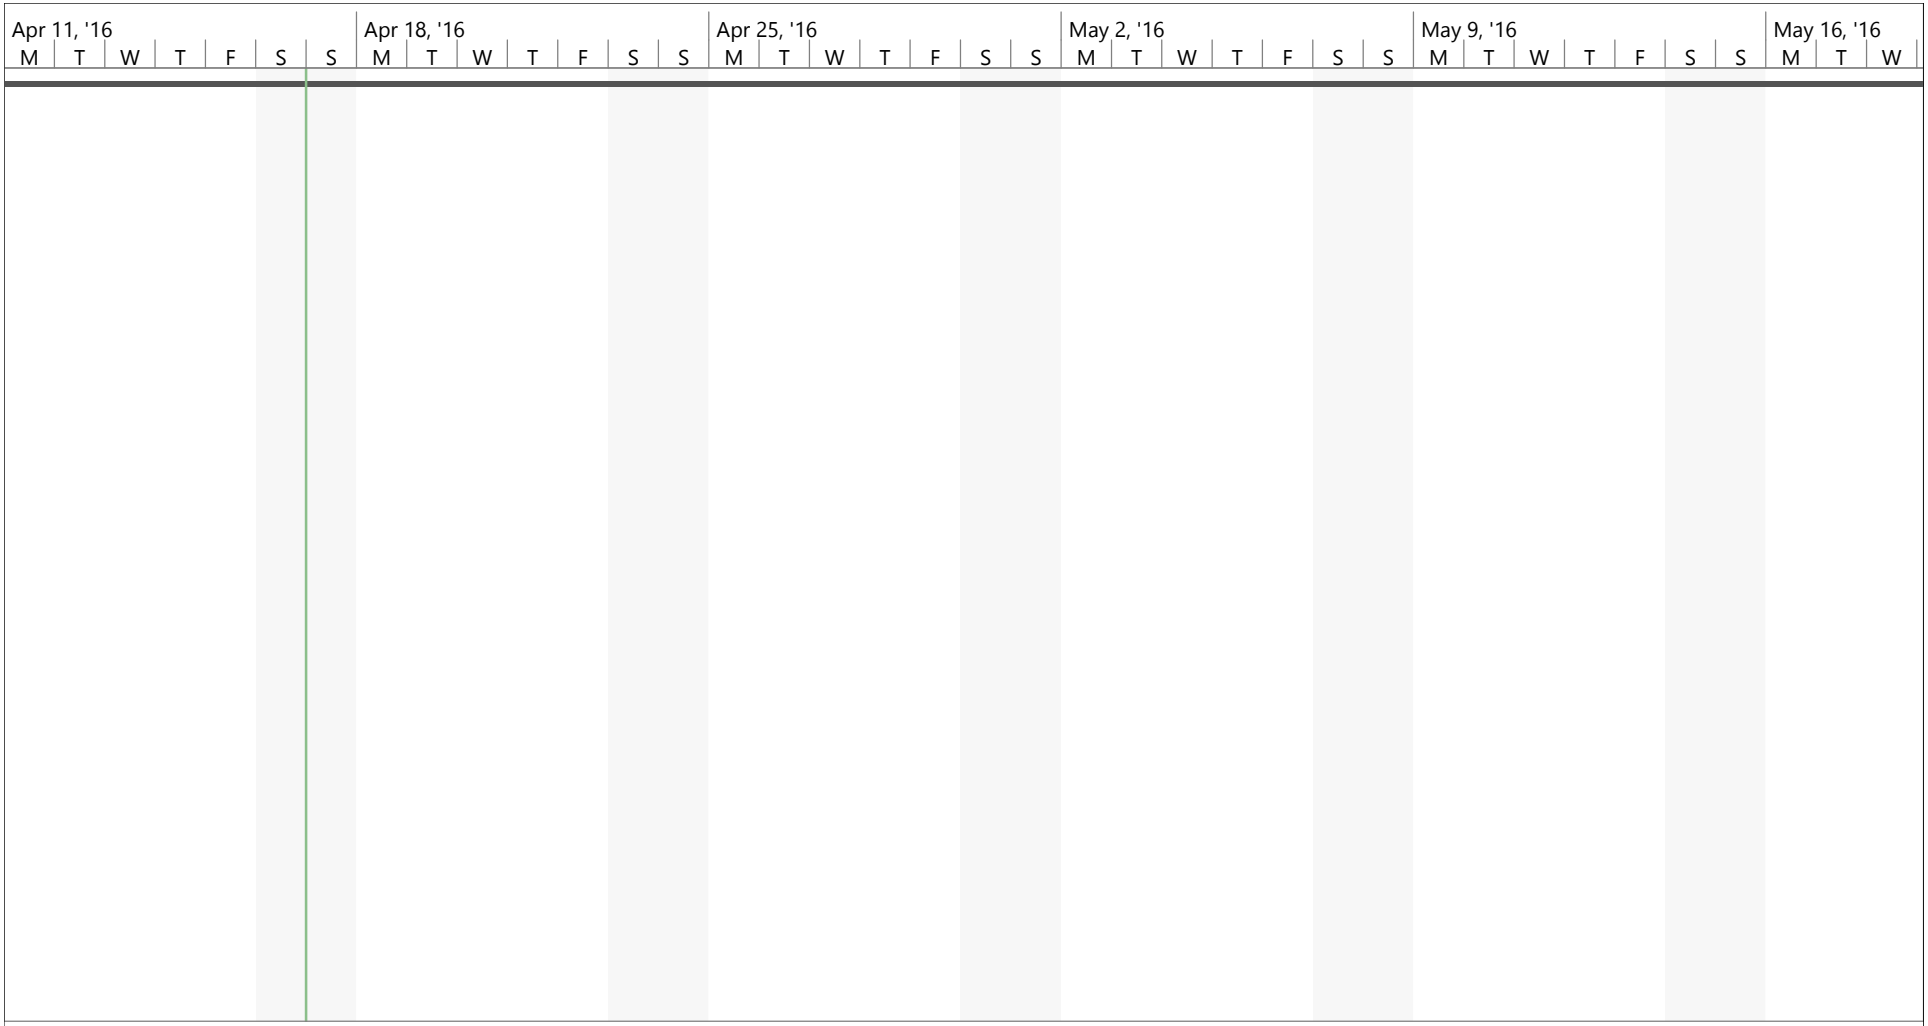

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

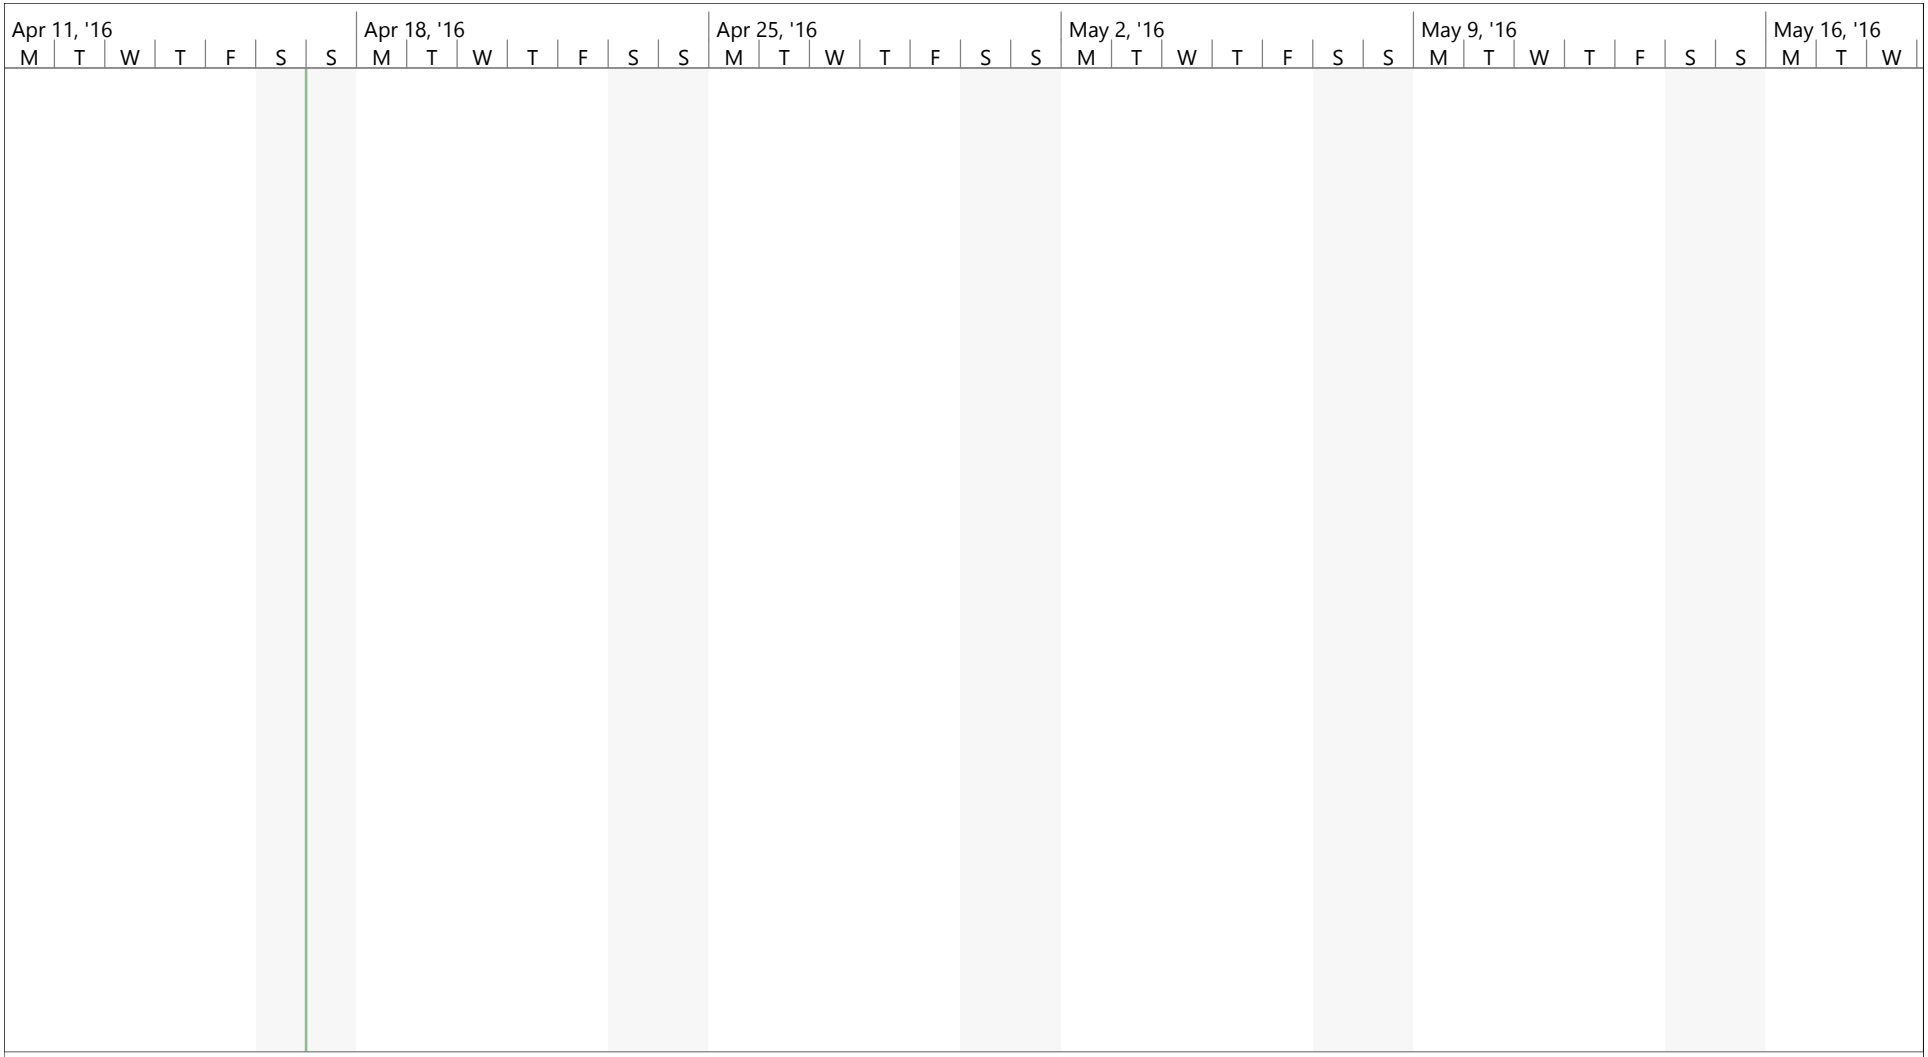

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

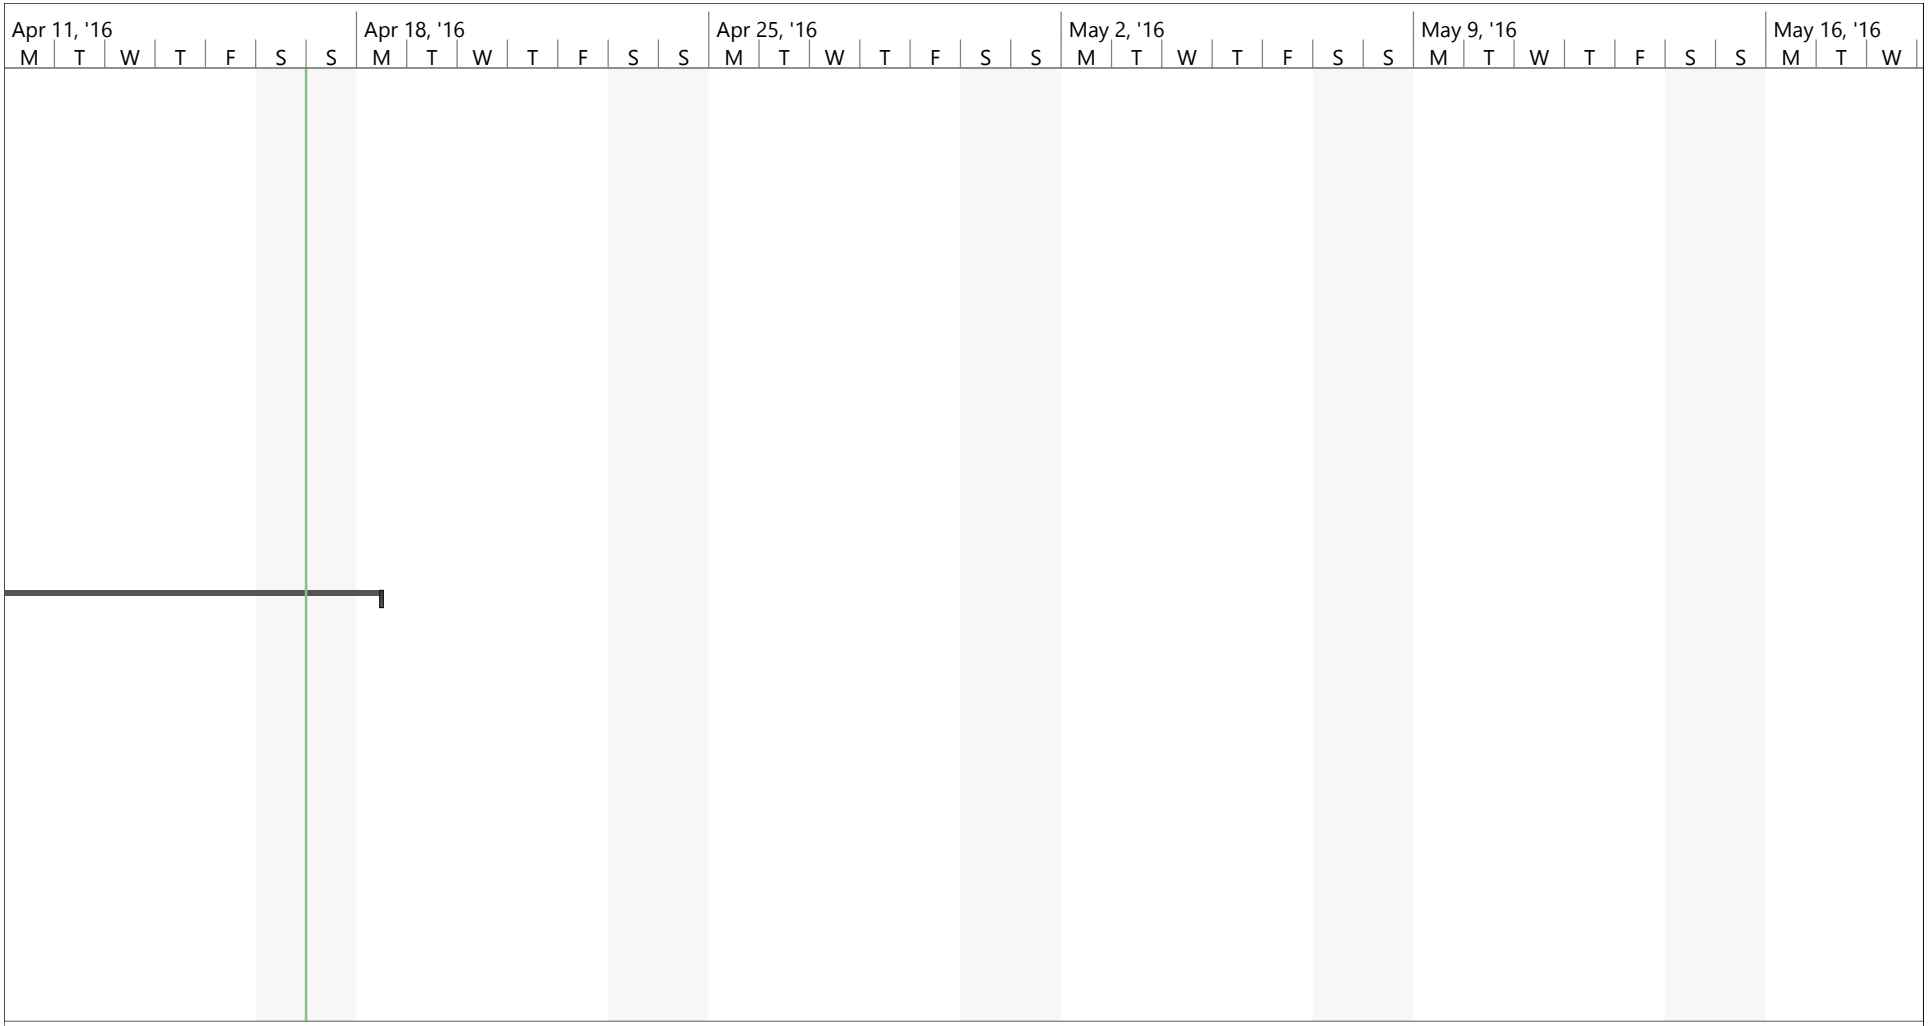

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

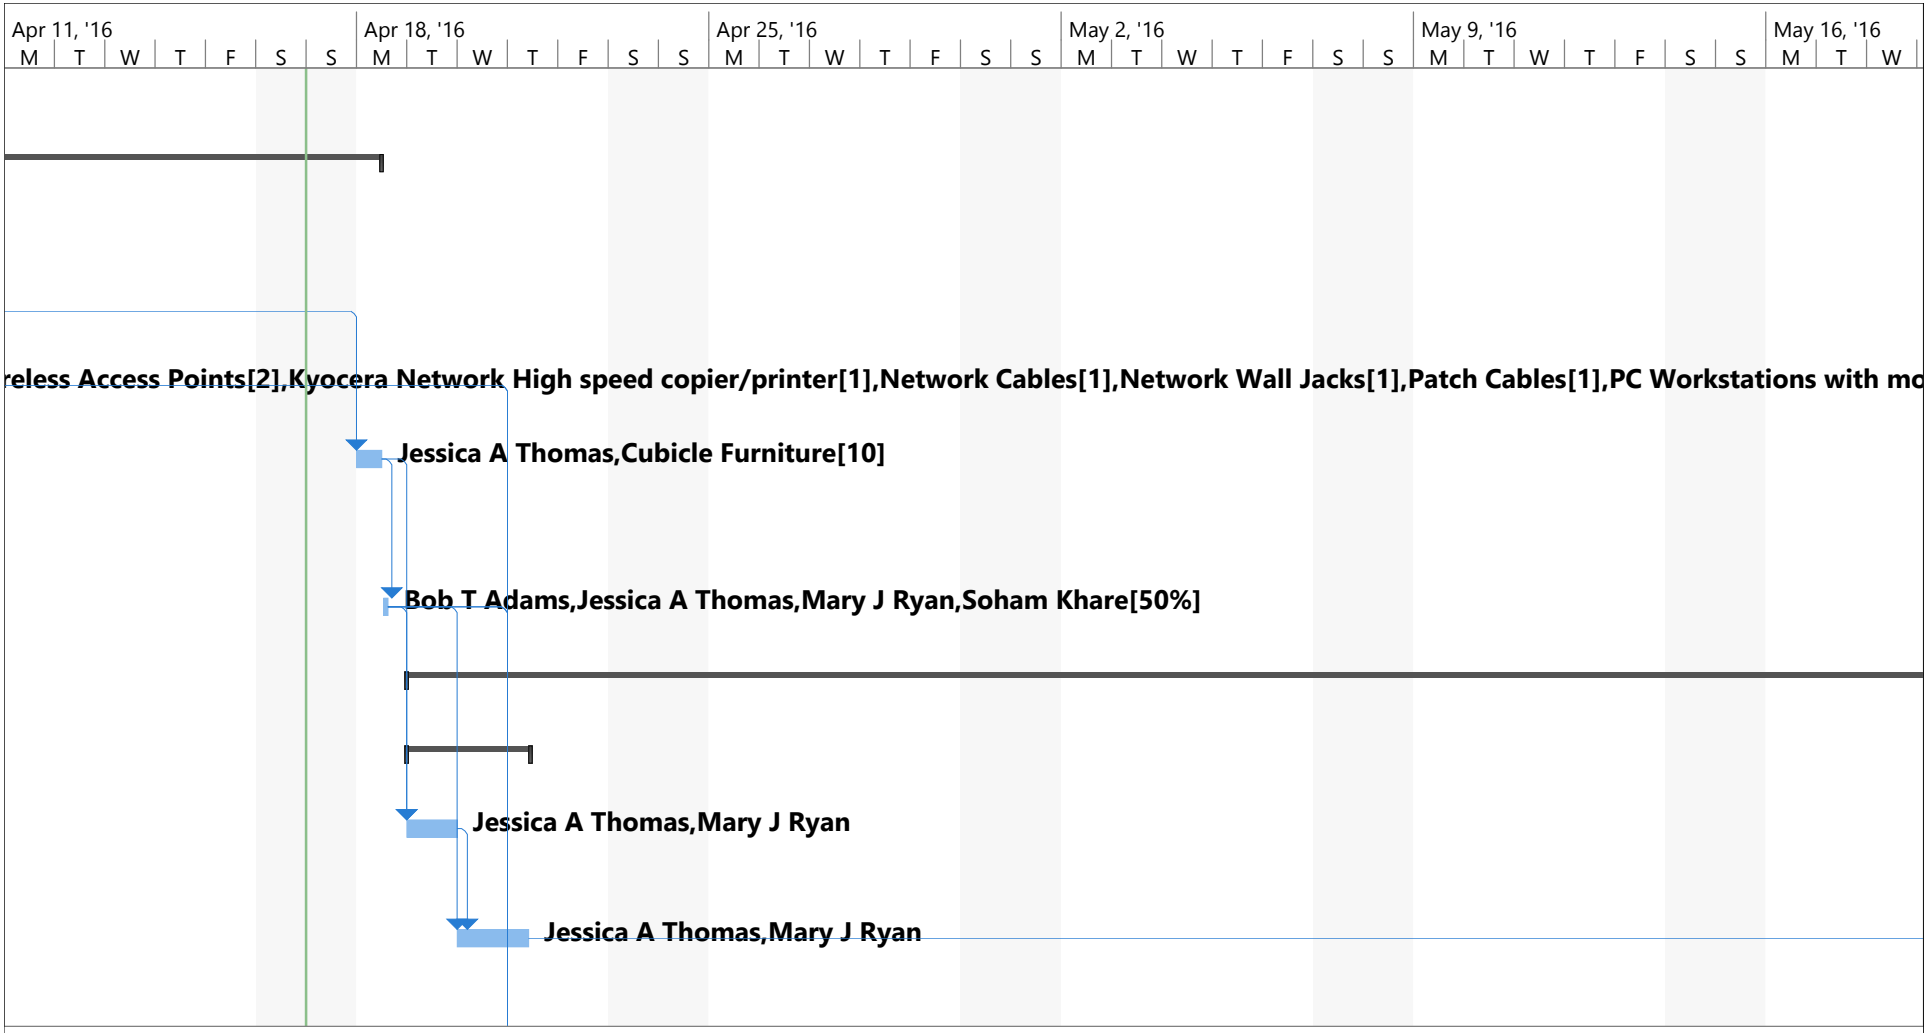

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

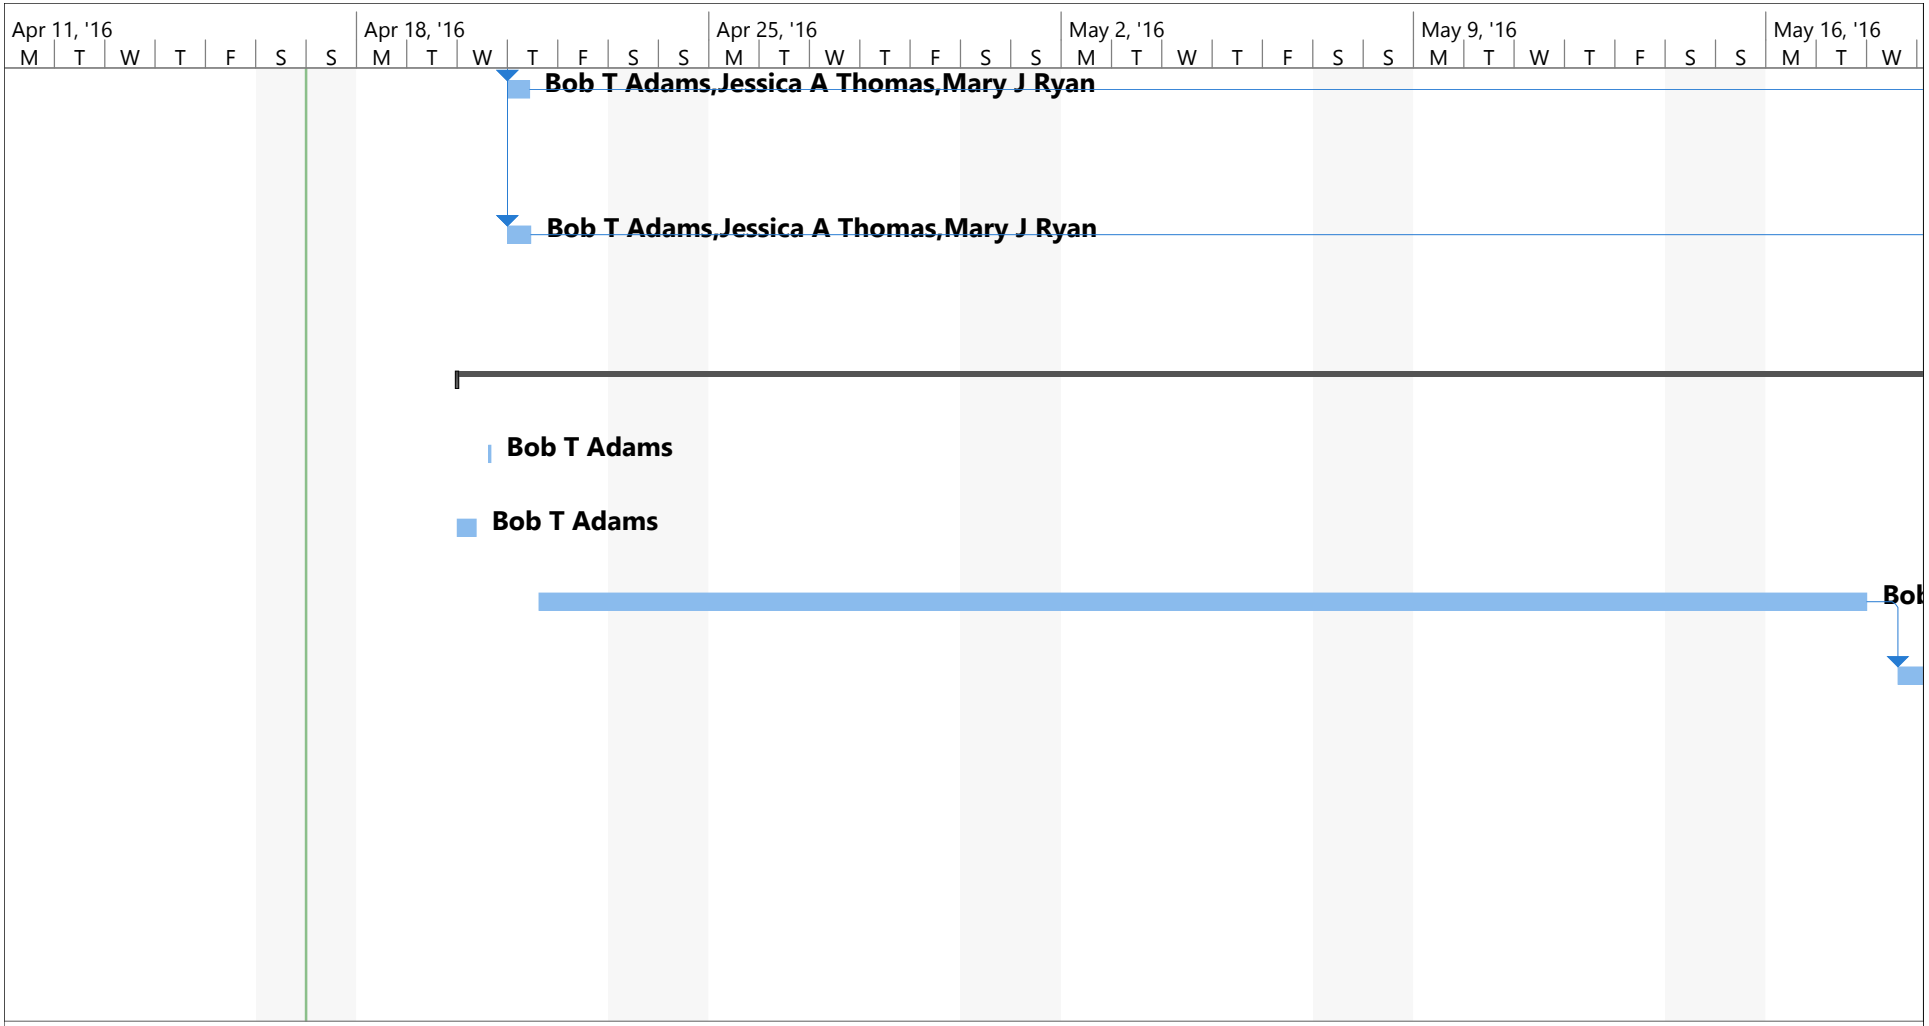

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

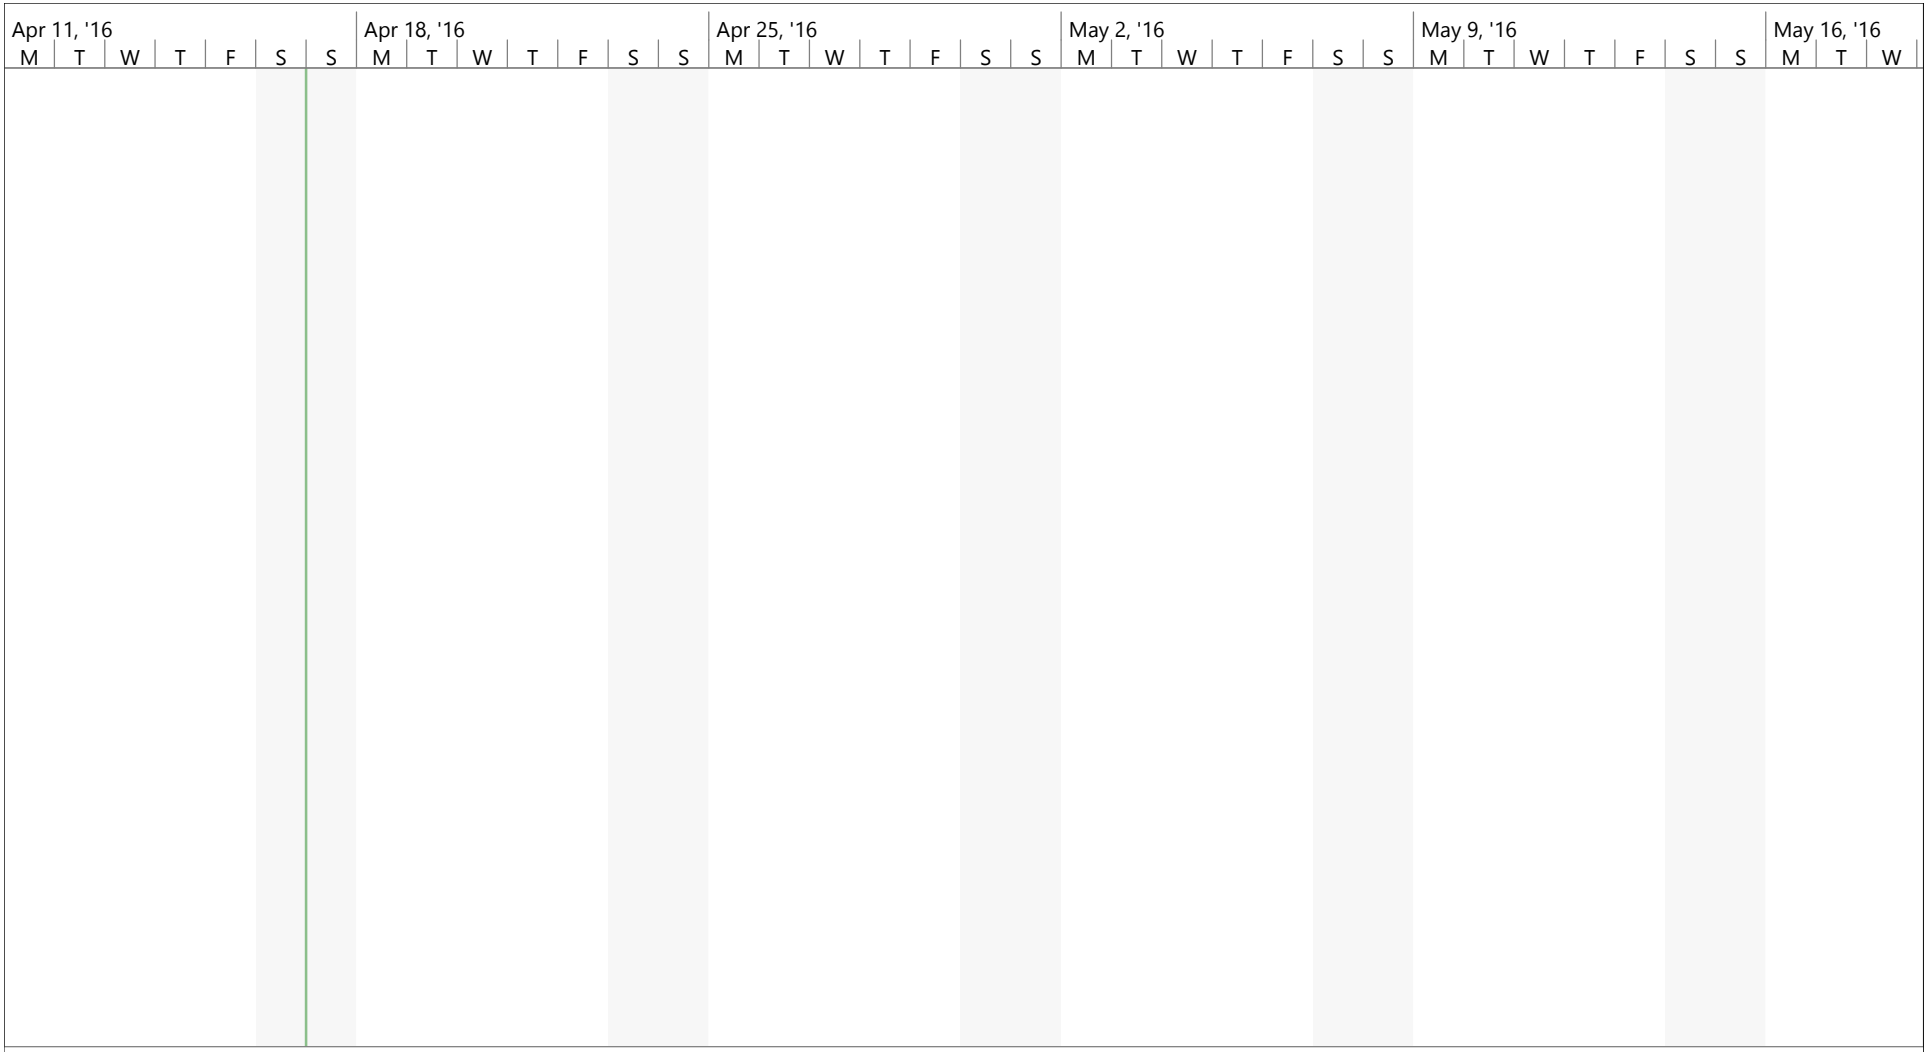

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

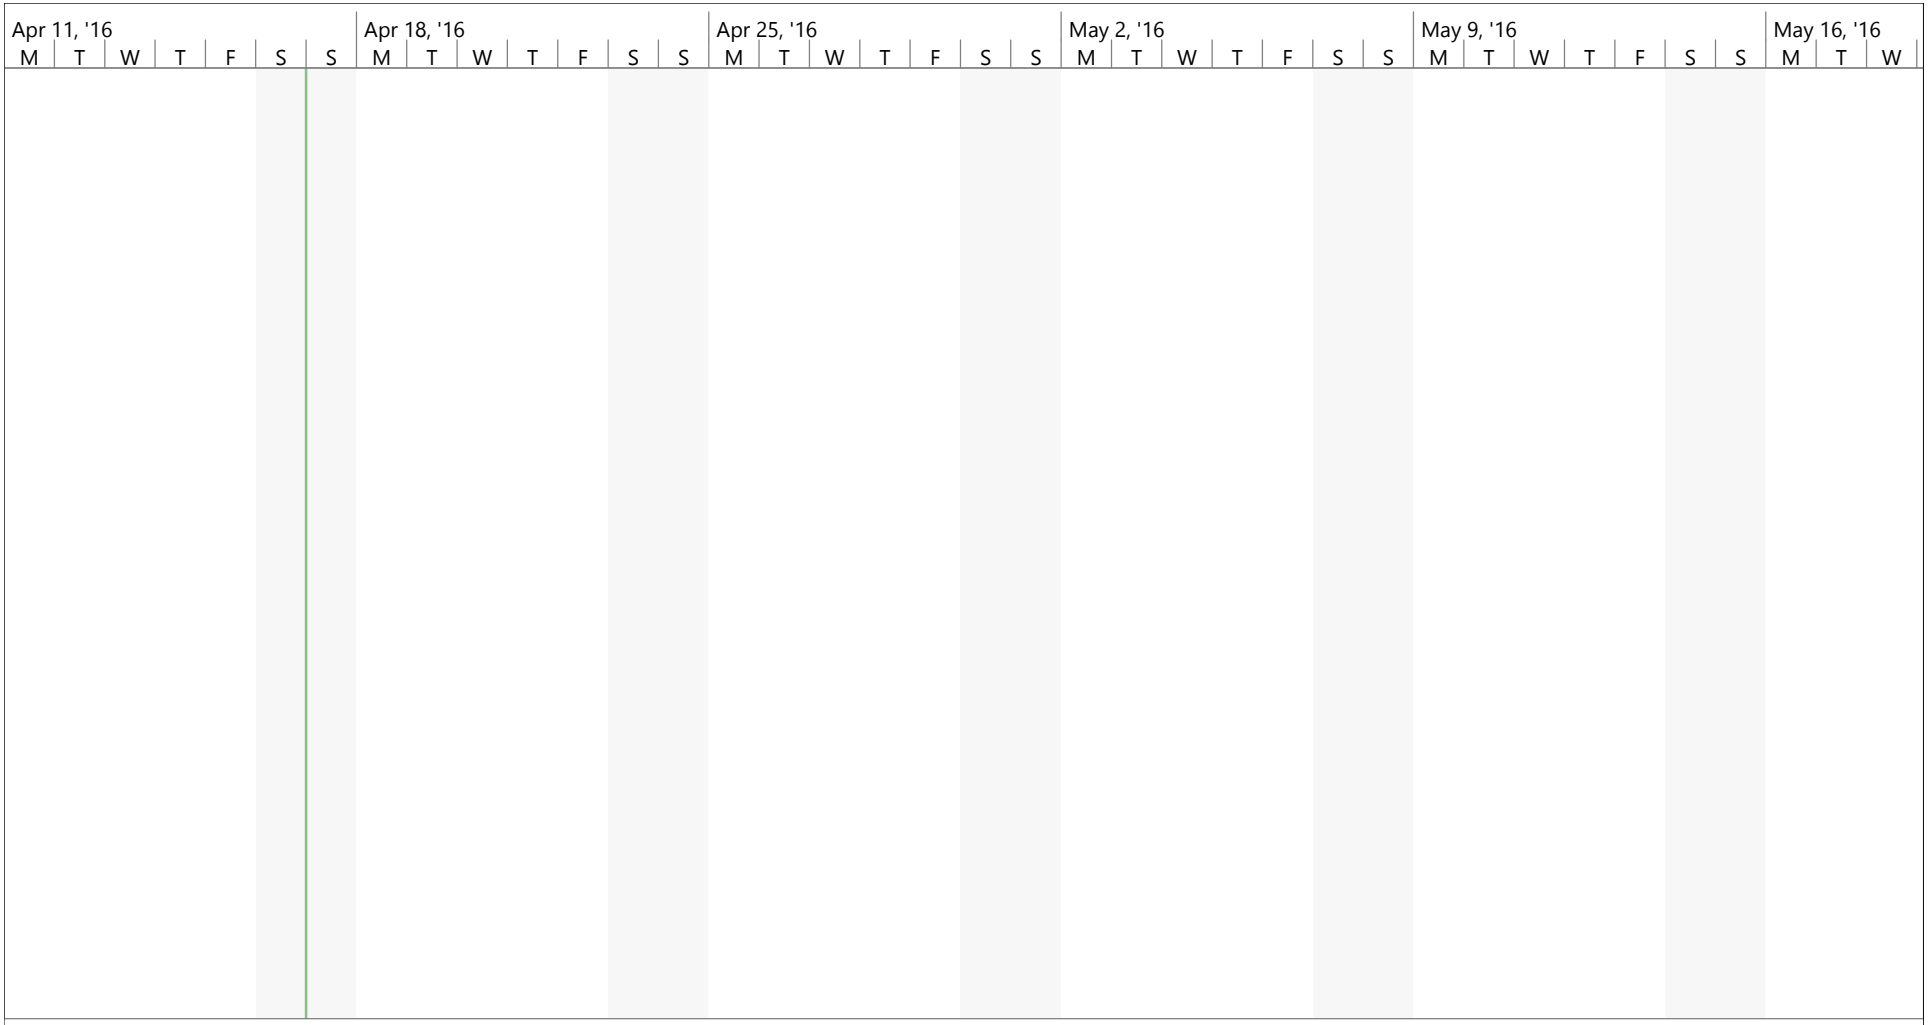

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			



Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

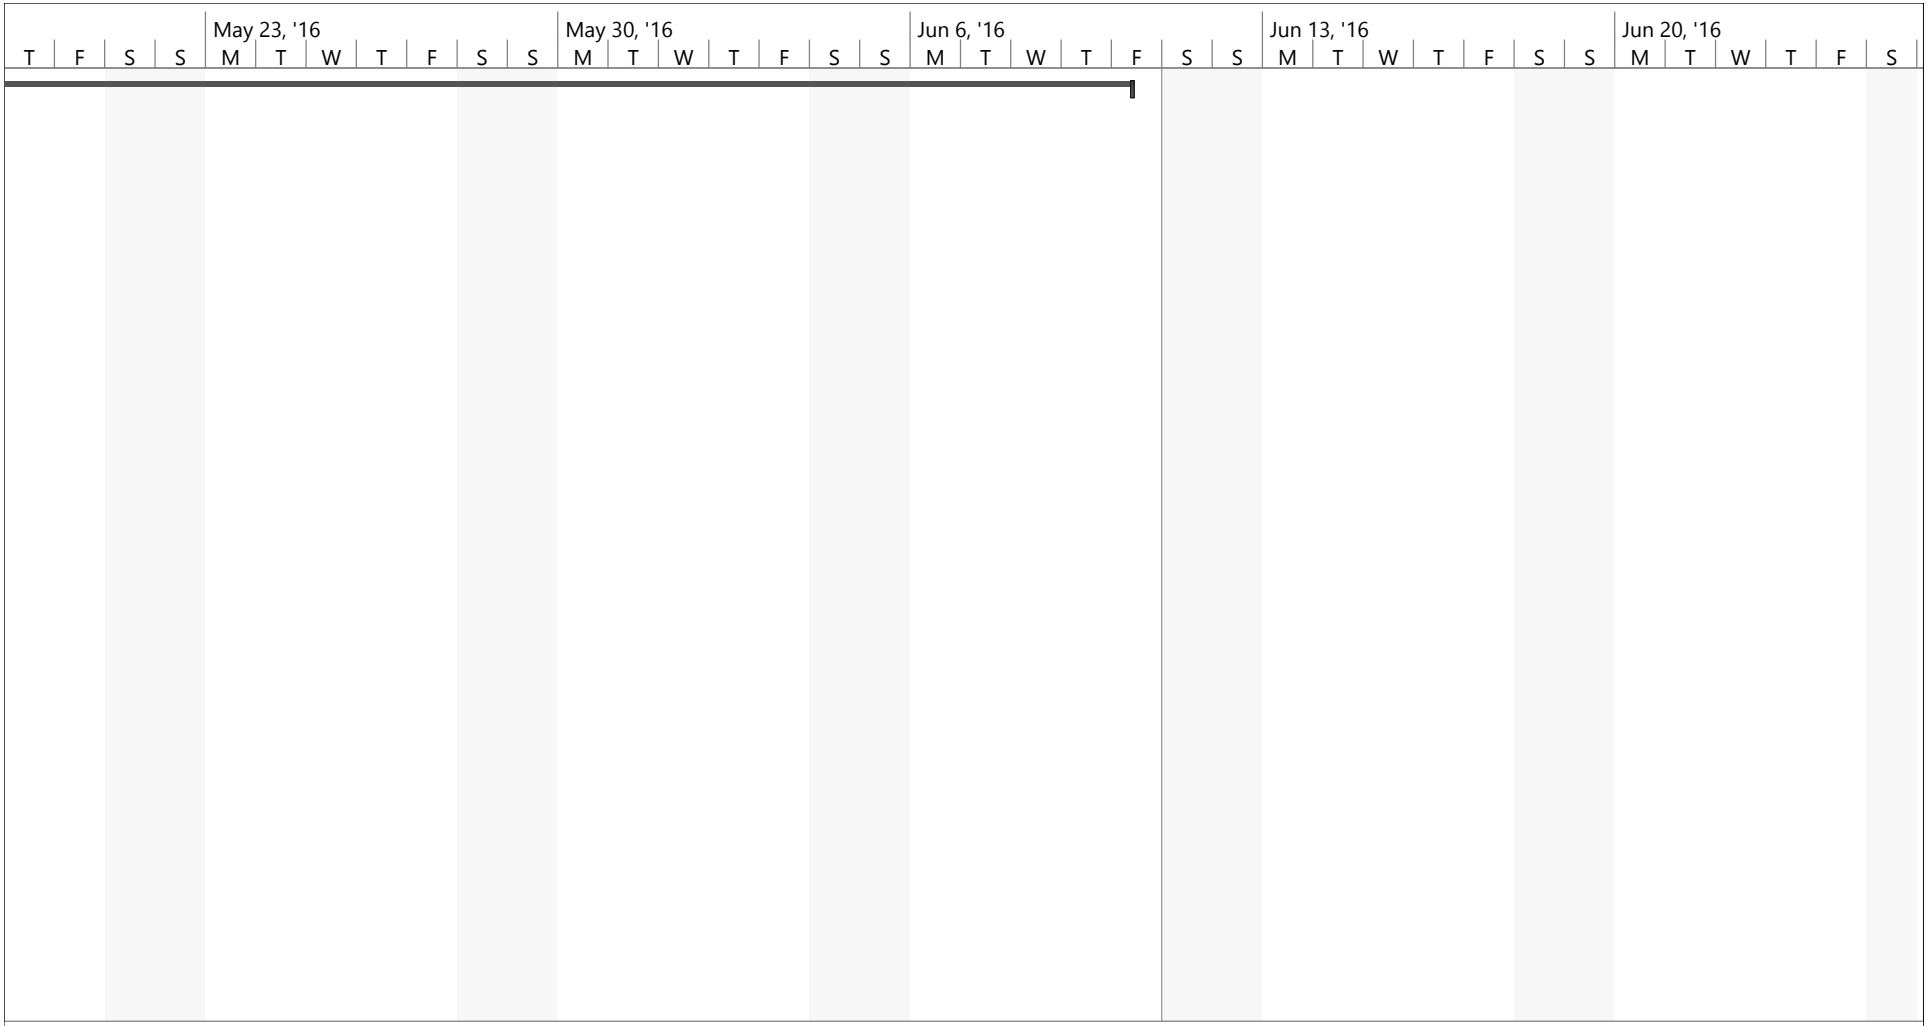

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

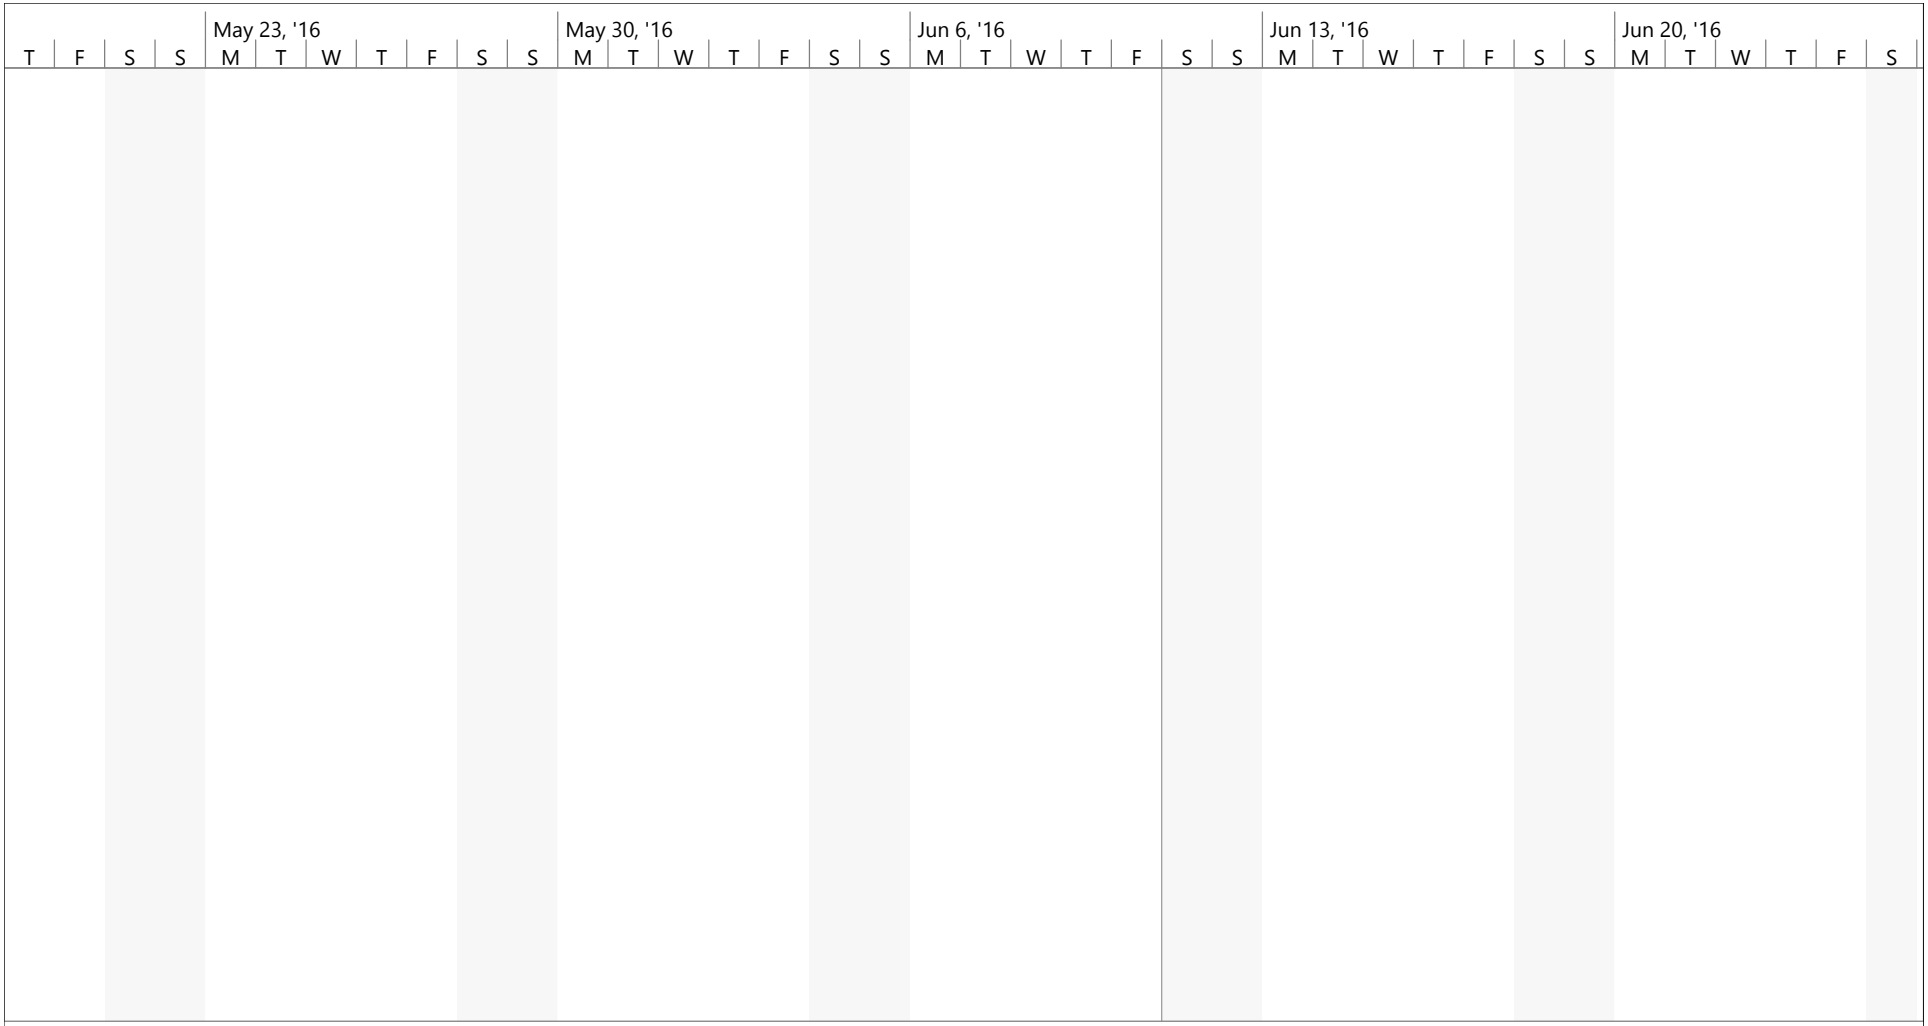

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

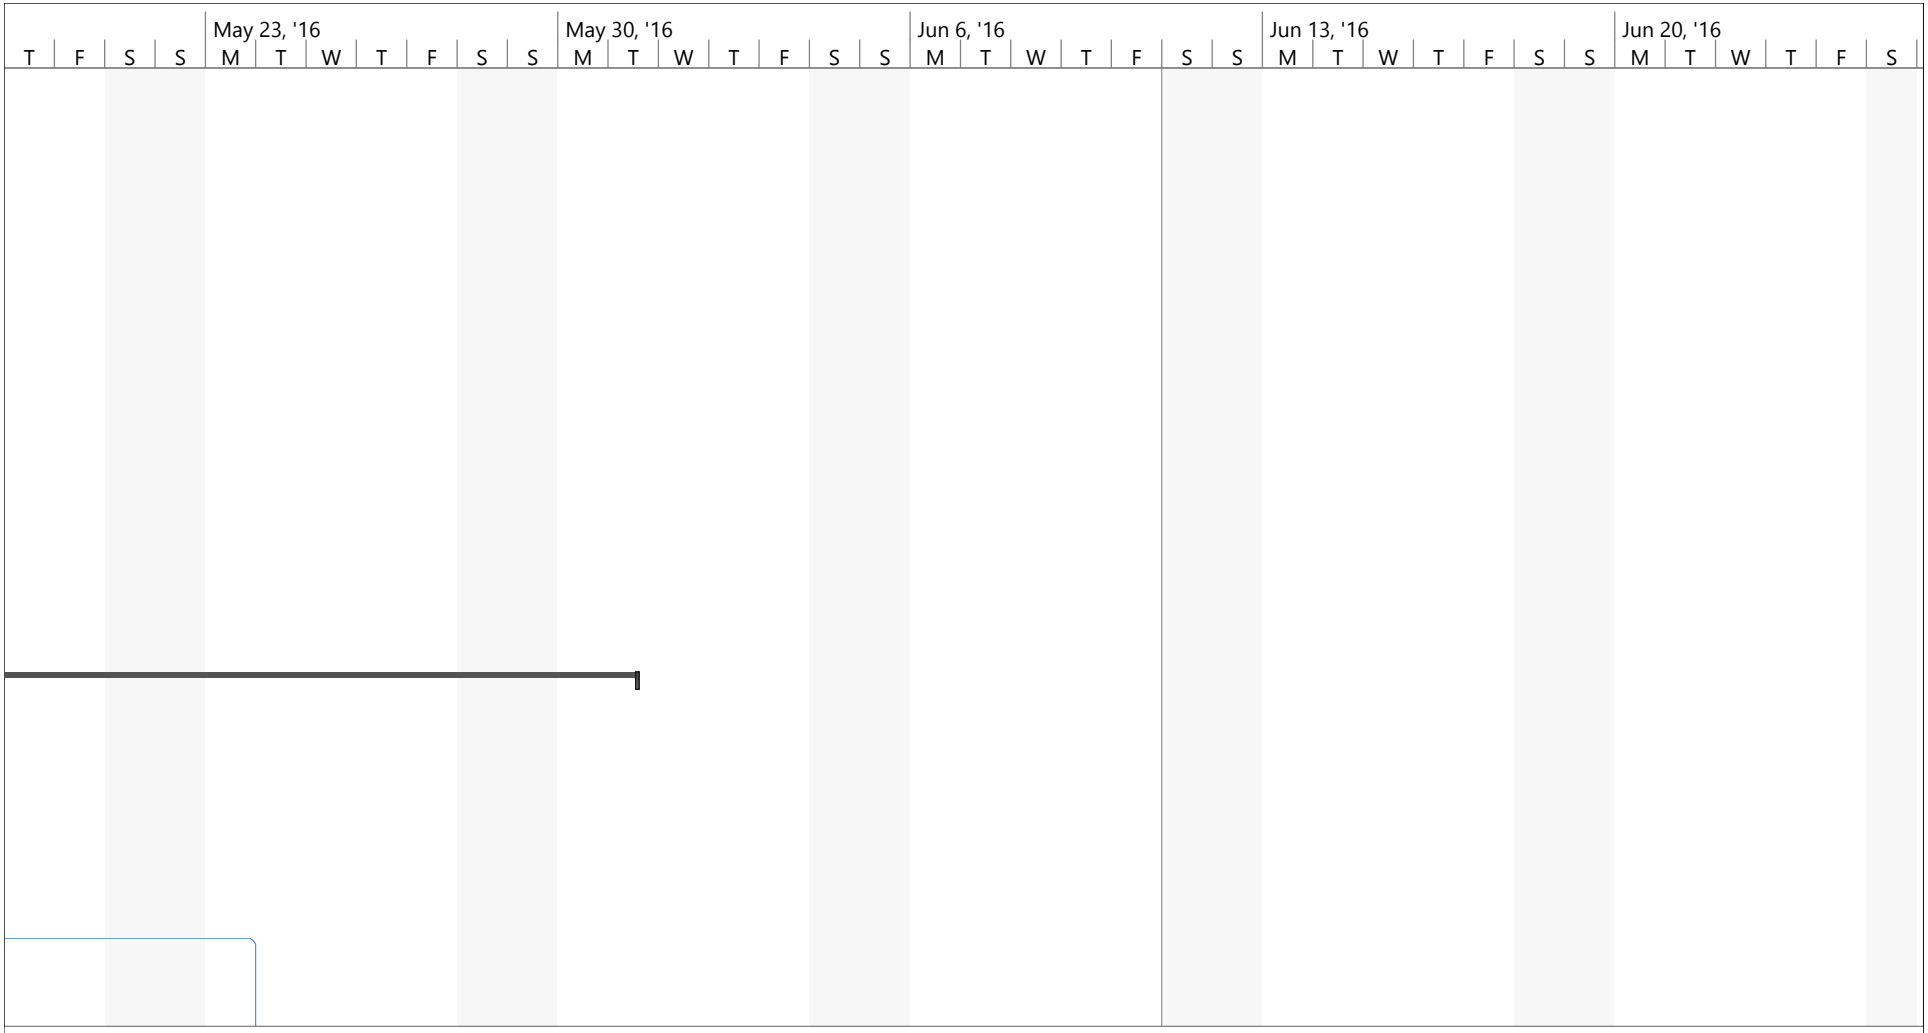

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

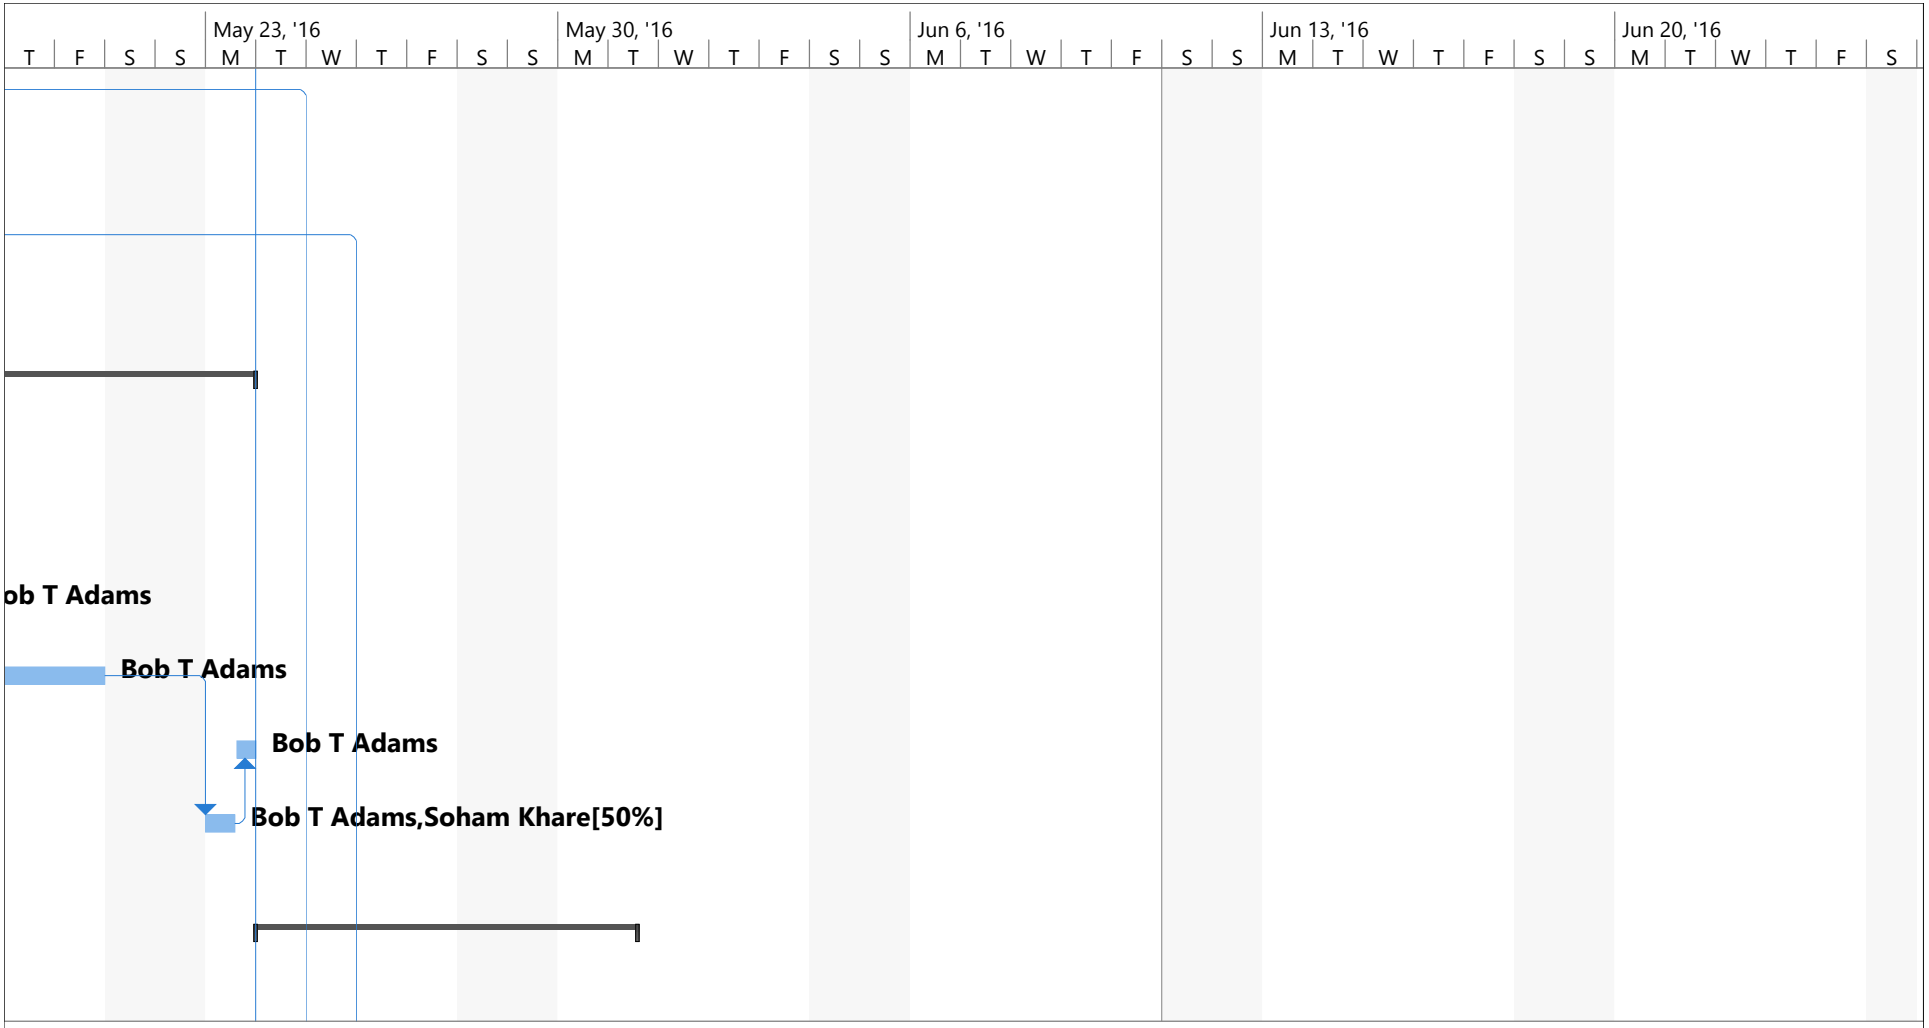

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

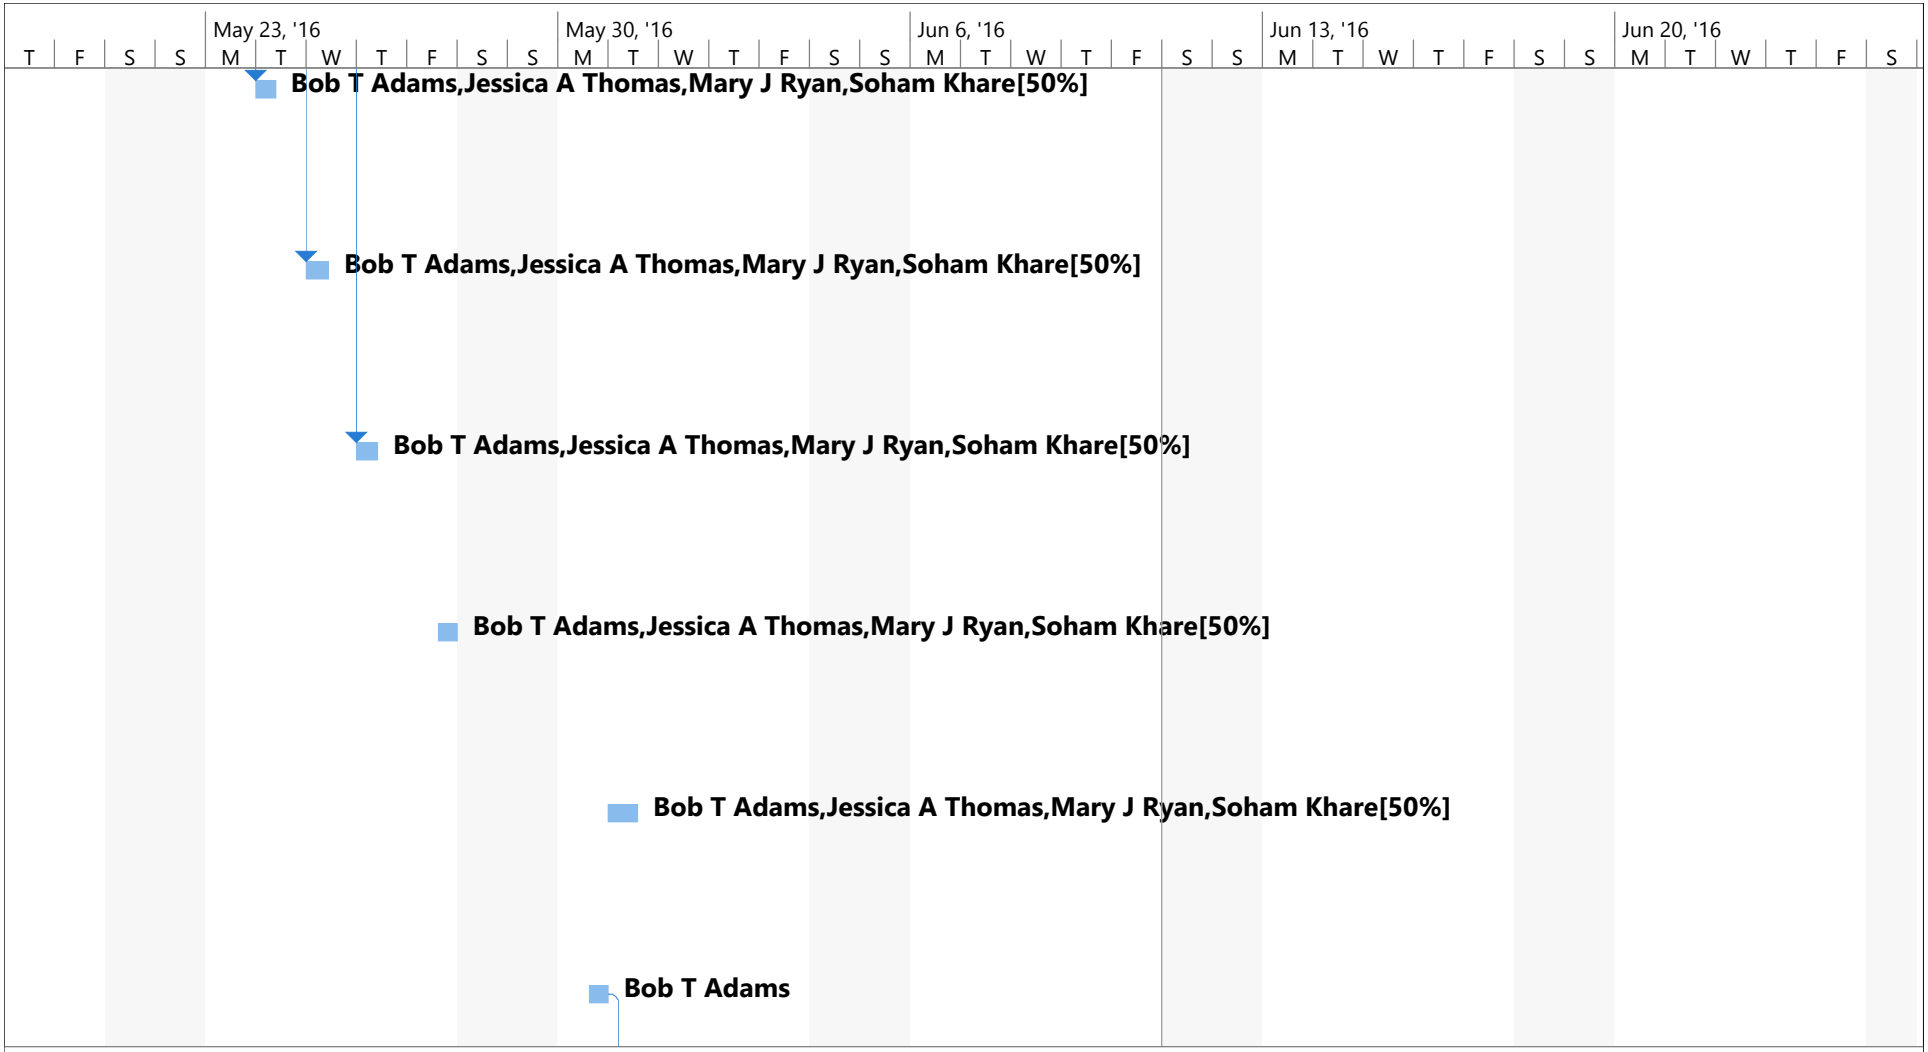

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task	Inactive Summary	External Tasks
Split	Manual Task	External Milestone
Milestone	Duration-only	Deadline
Summary	Manual Summary Rollup	Progress
Project Summary	Manual Summary	Manual Progress
Inactive Task	Start-only	
Inactive Milestone	Finish-only	

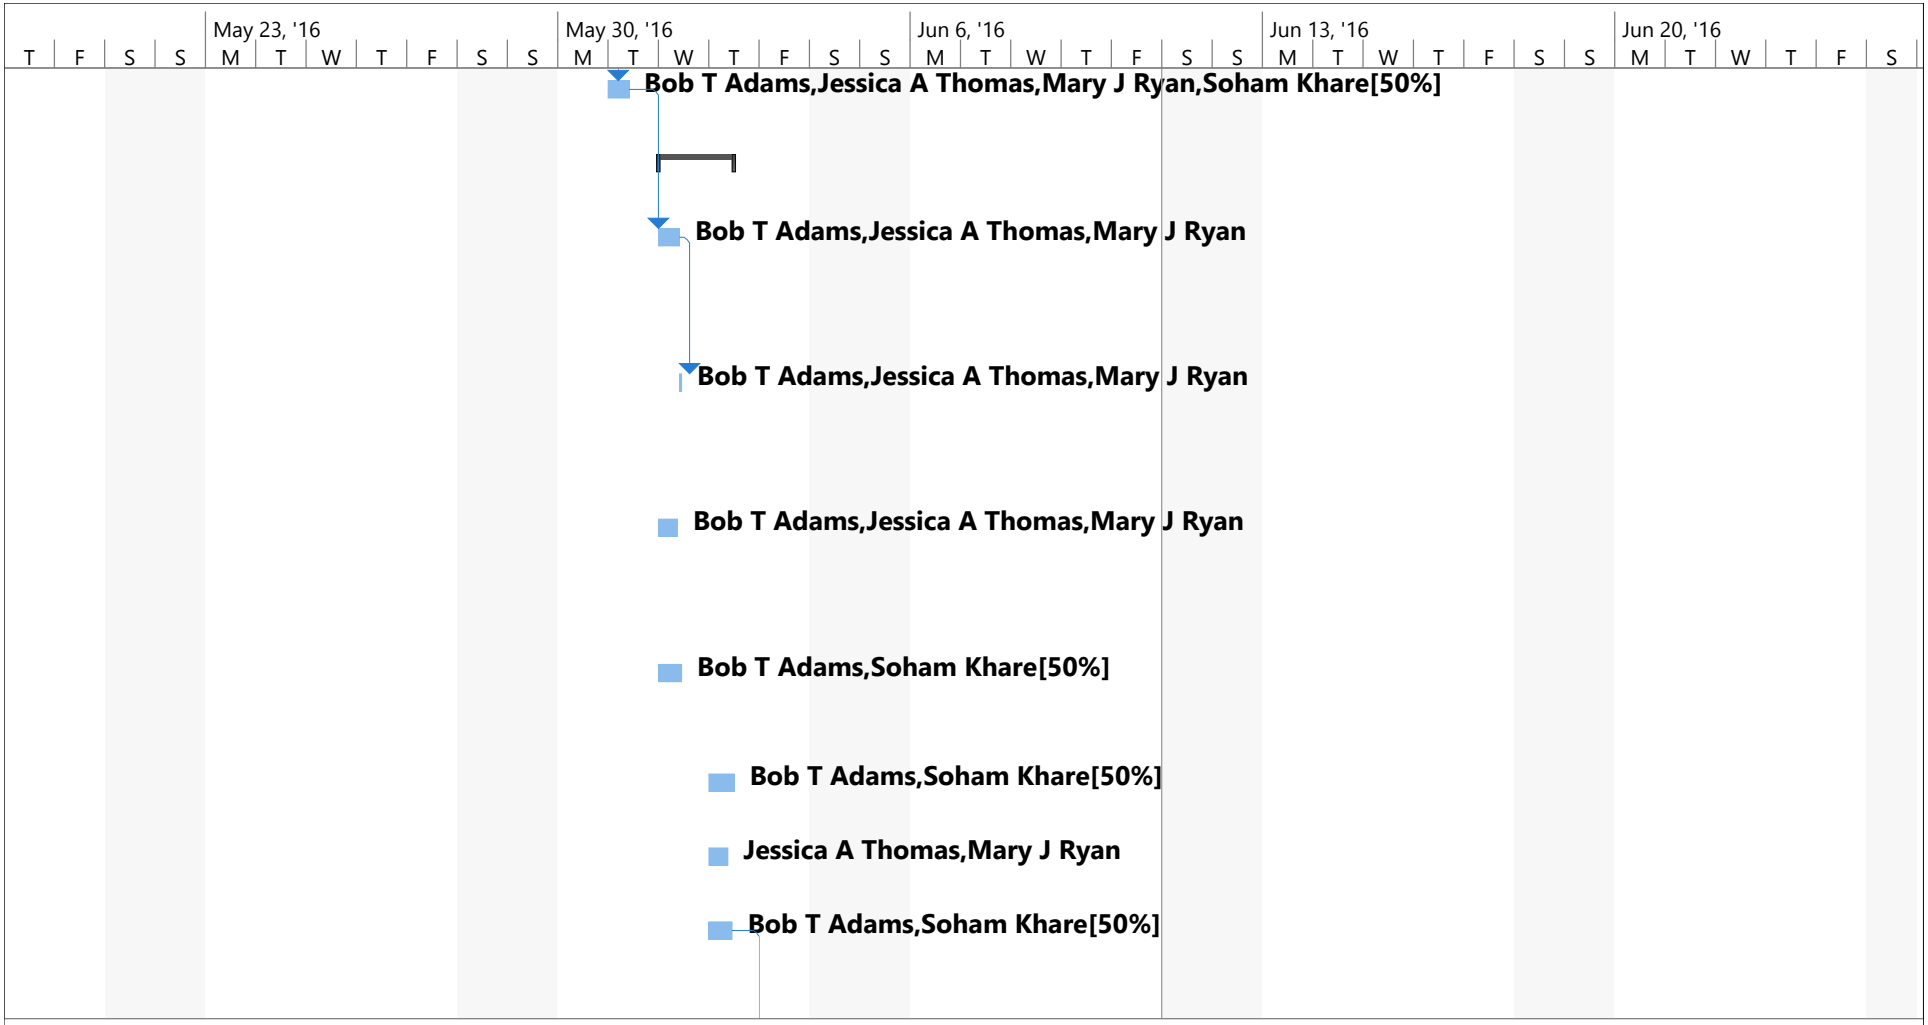

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

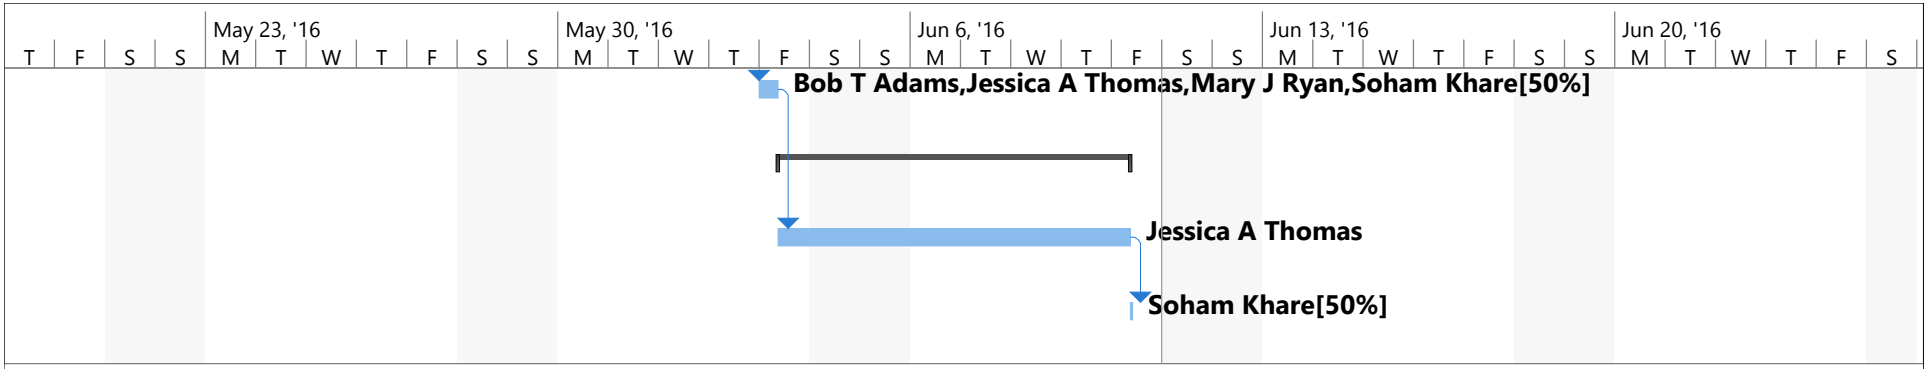

Project: FiberTel Infrastructure
Date: Sun 4/17/16

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			
